

Company: Southern California Gas Company (U 904 G)
Proceeding: 2024 General Rate Case
Application: A.22-05-XXX
Exhibit: (SCG-08-WP-S)

PUBLIC

SUPPLEMENTAL WORKPAPERS TO

PREPARED DIRECT TESTIMONY

OF BILL KOSTELNIK

ON BEHALF OF SOUTHERN CALIFORNIA GAS COMPANY

(PIPELINE SAFETY ENHANCEMENT PLAN)

VOLUME V OF VIII

BEFORE THE PUBLIC UTILITIES COMMISSION

OF THE STATE OF CALIFORNIA

MAY 2022



TABLE OF CONTENTS

| VOLUME | WORKPAPER CHAPTER TITLE | PAGE NO. |
|--|---|----------------|
| I. | Introduction to Workpapers Supporting the Testimony of Bill Kostelnik | WP-1 – 24 |
| | SCG Forecast Project Workpapers | WP-25 – 370 |
| II. | SCG Reasonableness Review Pipeline Project Workpapers | WP-371 – 798 |
| III. IV. V. | SCG Reasonableness Review Valve Enhancement Project Workpapers | WP-799 – 1917 |
| VI. | Construction Miscellaneous Costs | WP-1918 – 1921 |
| VII. | SCG Dairy Pilot Project Workpapers (non-PSEP) | WP-1922 – 1995 |
| VIII. | <i>Appendix A</i> – Summary of Standard Planning and Construction Practices for Replacement, Hydrotest, Valve, and Abandonment Projects | WP-A1 – A26 |
| | <i>Appendix B</i> – Glossary of Terms | WP-B1 – B15 |

VOLUME V

WP-1771 – 1917

SCG Reasonableness Review Valve Enhancement Project Workpapers (continued)

SCG Reasonableness Review Valve Enhancement Project Workpapers

REASONABLENESS REVIEW VALVE ENHANCEMENT PROJECTS

Table 3 – Valve Project Bundles submitted in the 2024 Reasonableness Review

| Valve Workpaper Title | Project Scope (valves, sites) | Workpaper Volume | Workpaper Page |
|---|--------------------------------------|-------------------------|-----------------------|
| 29 Palms Valve Enhancement Project - Indian Canyon | 1 valve, 1 site | III. | WP-799 |
| 29 Palms Valve Enhancement Project - Mohawk Trail | 1 valve, 1 site | III. | WP-815 |
| 29 Palms Valve Enhancement Project - Sunburst Street | 1 valve, 1 site | III. | WP-829 |
| 29 Palms Valve Enhancement Project - Utah Trail | 1 valve, 1 site | III. | WP-845 |
| 45-120 Valve Enhancement Project | 1 valve, 1 site | III. | WP-861 |
| 225 Valve Enhancement Project - Beartrap | 1 valve, 1 site | III. | WP-878 |
| 225 Valve Enhancement Project - Quail Canal | 1 valve, 1 site | III. | WP-894 |
| 404-406 Valley Bundle Valve Enhancement Project | 8 valves, 4 sites | III. | WP-910 |
| 404-406 Ventura Valve Enhancement Project - Somis Yard | 1 valve, 1 site | III. | WP-941 |
| 1014 Olympic Valve Enhancement Project | 6 valves, 2 sites | III. | WP-957 |
| 1018 Valve Enhancement Project - Alipaz Street | 1 valve, 1 site | III. | WP-979 |
| 1018 Valve Enhancement Project - Avery Parkway | 1 valve, 1 site | III. | WP-995 |
| 1018 Valve Enhancement Project - Burt Road | 2 valves, 1 site | III. | WP-1012 |
| 1018 Valve Enhancement Project - Camino Capistrano | 1 valve, 1 site | III. | WP-1029 |
| 1018 Valve Enhancement Project - El Toro Road | 1 valve, 1 site | III. | WP-1047 |
| 1018 Valve Enhancement Project - Harvard & Alton | 3 valves, 1 site | III. | WP-1065 |
| 2000 Beaumont Riverside 2016 Valve Enhancement Project Bundle | 4 valves, 4 sites | III. | WP-1083 |
| 4000 Valve Enhancement Project - Camp Rock Road | 1 valve, 1 site | III. | WP-1110 |
| 4000 Valve Enhancement Project - Desert View Road | 1 valve, 1 site | III. | WP-1126 |
| 4000 Valve Enhancement Project - Devore Station | 2 valves, 1 site | III. | WP-1142 |
| 4000 Valve Enhancement Project - Powerline Road | 1 valve, 1 site | III. | WP-1158 |
| 4002 Fontana Valve Enhancement Project - Etiwanda & 4th | 1 valve, 1 site | III. | WP-1174 |
| 7000 Valve Enhancement Project - Beech & Highway 46 | 1 valve, 1 site | III. | WP-1191 |
| 7000 Valve Enhancement Project - Melcher & Elmo | 3 valves, 1 site | III. | WP-1208 |
| 7000 Valve Enhancement Project - Road 68 & Avenue 232 | 1 valve, 1 site | III. | WP-1226 |
| 7000 Valve Enhancement Project - Road 96 & Avenue 198 | 1 valve, 1 site | III. | WP-1242 |
| 7000 Valve Enhancement Project - Visalia Station | 2 valves, 1 site | III. | WP-1258 |
| Adelanto Valve Enhancement Project - MLV 4 | 1 valve, 1 site | III. | WP-1276 |
| Apple Valley Valve Enhancement Project - MLV 2 | 1 valve, 1 site | IV. | WP-1291 |
| Apple Valley Valve Enhancement Project - MLV 13 | 1 valve, 1 site | IV. | WP-1307 |
| Aviation & 104th Valve Enhancement Project | 5 valves, 1 site | IV. | WP-1324 |
| Banning 2001 Valve Enhancement Project - MLV 14.3A | 3 valves, 1 site | IV. | WP-1345 |
| Banning 2001 Valve Enhancement Project - MLV 14A | 1 valve, 1 site | IV. | WP-1361 |
| Banning 2001 Valve Enhancement Project - MLV 16A | 1 valve, 1 site | IV. | WP-1377 |

REASONABLENESS REVIEW VALVE ENHANCEMENT PROJECTS

| Valve Workpaper Title | Project Scope (valves, sites) | Workpaper Volume | Workpaper Page |
|---|--------------------------------------|-------------------------|-----------------------|
| Banning 2001 Valve Enhancement Project - MLV 17A | 1 valve, 1 site | IV. | WP-1394 |
| Banning Airport Valve Enhancement Project | 2 valves, 1 site | IV. | WP-1410 |
| Blythe Valve Enhancement Project - Cactus City | 1 valve, 1 site | IV. | WP-1427 |
| Brea Valve Enhancement Project - Atwood Station | 3 valves, 1 site | IV. | WP-1442 |
| Brea Valve Enhancement Project - Carbon Canyon | 1 valve, 1 site | IV. | WP-1458 |
| Brea Valve Enhancement Project - Gale & Azusa | 1 valve, 1 site | IV. | WP-1474 |
| Brea Valve Enhancement Project - Brea Canyon | 3 valves, 1 site | IV. | WP-1490 |
| Burbank Valve Enhancement Project - Riverside & Agnes | 1 valve, 1 site | IV. | WP-1507 |
| Carpinteria Valve Enhancement Project - Oxy & Rincon | 1 valve, 1 site | IV. | WP-1522 |
| Del Amo Station Valve Enhancement Project | 3 valves, 1 site | IV. | WP-1538 |
| Fontana 4000-4002 Valve Enhancement Project - Benson & Chino | 1 valve, 1 site | IV. | WP-1554 |
| Glendale Valve Enhancement Project - Geneva & Monterey | 1 valve, 1 site | IV. | WP-1574 |
| Indio Valve Enhancement Project - MLVs 8, 8A, & 8B | 3 valves, 2 sites | IV. | WP-1589 |
| Indio Valve Enhancement Project - MLV 9A & 9B | 2 valves, 1 site | IV. | WP-1609 |
| Indio Valve Enhancement Project - MLVs 10, 10A, & 10B | 3 valves, 1 site | IV. | WP-1627 |
| Palowalla Valve Enhancement Project | 3 valves, 1 site | IV. | WP-1645 |
| Rainbow 2017 Valve Enhancement Project - Martin & Ramona | 2 valves, 1 site | IV. | WP-1661 |
| Rainbow Check Valve Enhancement Project - Newport & Briggs | 1 valve, 1 site | IV. | WP-1676 |
| Rainbow Check Valve Enhancement Project - Scott & El Centro | 2 valves, 1 site | IV. | WP-1691 |
| Rainbow Check Valve Enhancement Project - Rainbow Valley & Pechanga | 2 valves, 1 site | IV. | WP-1706 |
| Rainbow CV Valve Enhancement Project - Ramona & Lakeview | 2 valves, 1 site | IV. | WP-1722 |
| Rainbow Valve Enhancement Project - MLV 5 | 3 valves, 1 site | IV. | WP-1738 |
| Santa Barbara County Valve Enhancement Project - Lions | 1 valve, 1 site | IV. | WP-1754 |
| Spence Station Valve Enhancement Project | 1 valve, 1 site | V. | WP-1771 |
| Taft Valve Enhancement Project - 7th Standard | 1 valve, 1 site | V. | WP-1786 |
| Taft Valve Enhancement Project - Buttonwillow | 1 valve, 1 site | V. | WP-1802 |
| Taft Valve Enhancement Project - Hageman & Renfro | 2 valves, 1 site | V. | WP-1818 |
| Taft Valve Enhancement Project – Sycamore Road | 1 valve, 1 site | V. | WP-1838 |
| Victorville COMMS Valve Enhancement Project - MLV 11 | 1 valve, 1 site | V. | WP-1854 |
| Victorville COMMS Valve Enhancement Project - MLV 12 | 1 valve, 1 site | V. | WP-1870 |
| Western Del Rey Valve Enhancement Project - Mississippi & Armacost | 1 valve, 1 site | V. | WP-1886 |
| Wilmington Valve Enhancement Project - Eubank Station | 2 valves, 1 site | V. | WP-1902 |

Final Report for Spence Station Valve Enhancement Project

I. SPENCE STATION VALVE ENHANCEMENT PROJECT

A. Background and Summary

The Spence Station Valve Enhancement Project Spence Station consists of valve enhancements made to one existing mainline valve (MLV) located in the City of Los Angeles. Through this project, SoCalGas enhanced the safety of its natural gas transmission system by enabling the rapid detection of a significant change in pipeline pressure and remote isolation and depressurization of a portion of Line 765 in the event of a pipeline rupture. SoCalGas installed a new actuator, a new flowmeter, a new vault to house the flowmeter, and the necessary automation equipment. The total loaded project cost is \$1,703,874.

The Spence Station Valve Enhancement Project construction site is within an existing SoCalGas facility in an industrial area in the City of Los Angeles. All work was done within the station where there was sufficient space for a laydown yard.

Final Report for Spence Station Valve Enhancement Project

Table 1: General Project Information

| Spence Station Valve Enhancement Project | | | |
|---|--------------------|----------------|--------------|
| Location | Los Angeles | | |
| Days on Site | 36 days | | |
| Construction Start | 12/14/2017 | | |
| Construction Finish | 03/15/2018 | | |
| Commissioning Date | 09/04/2019 | | |
| Valve Upgrades | | | |
| Valve Number | 765-12.36-0 | | |
| Valve Type | Existing – Ball | | |
| Actuator | New | | |
| Actuator Above-/Below-Grade | Above-Grade | | |
| ASV | Yes | | |
| RCV | Yes | | |
| Valve Number | 2000-222.71-FM | | |
| Valve Type | Flow Meter | | |
| Actuator | N/A | | |
| Actuator Above-/Below-Grade | N/A | | |
| ASV | N/A | | |
| RCV | N/A | | |
| Spence Station Site Upgrades | | | |
| Vault | New | | |
| Power | Existing – Utility | | |
| Communication | Existing – Radio | | |
| SCADA Panel | New | | |
| Equipment Shelter | Existing | | |
| Fencing/Wall | Existing | | |
| Project Costs (\$) | Capital | O&M | Total |
| Loaded Project Costs | 1,703,874 | - | 1,703,874 |
| Disallowed Costs | - | - | - |

Final Report for Spence Station Valve Enhancement Project

II. ENGINEERING, DESIGN, AND PLANNING

A. Project Scope

SoCalGas and SDG&E presented a conceptual project scope for the Spence Station Valve Enhancement Project in workpapers supporting the Valve Enhancement Plan in the 2011 filing.¹ This conceptual scope identified valves 765-12.36-0, 765-12.36-1 and 765-12.36-2 for automation to enable remote isolation to a portion of Line 765. Prior to initiating execution of the Project, SoCalGas reviewed available information and performed a detailed system flow analysis to validate the scope of the Project and identified an additional valve for enhancement to provide the planned isolation. SoCalGas also identified this location as one of the candidates for flowmeter installation. Prior to TIC, the Project Team descoped valves 765-12.36-1 and 765-12.36-2 from the project scope. The final project scope is summarized in Table 2 below.

1. 2011 PSEP Filing: SoCalGas and SDG&E identified valves 765-12.36-0, 765-12.36-1, and 765-12.36-2 for automation to achieve the objective of rapid system isolation.
2. Updated Scope: Upon project initiation, SoCalGas reviewed the conceptual project scope and determined that these isolation points would alone not achieve the transmission isolation objectives set forth in the Valve Enhancement Plan. SoCalGas reevaluated the isolation points at valves 765-12.36-0, 765-12.36-1, and 765-12.36-2 and determined that the automation of valve 765-12.36-4 would better achieve the objectives set forth in the Valve Enhancement Plan. SoCalGas also determined that this is an ideal location for the installation of a flow meter, thereby achieving Valve Enhancement Plan objectives.

¹ See Workpapers supporting Amended Pipeline Safety Enhancement Plan (PSEP) of SoCalGas and SDG&E, submitted on December 2, 2011, at WP-IX-2-14 through WP-IX-2-25 (A.11-11-002 Exh. SCG-32).

Final Report for Spence Station Valve Enhancement Project

3. Engineering, Design, and Constructability:
 - a. The Project Team determined that valve 765-12.36-1 is normally closed and did not require automation to achieve Valve Enhancement Plan objectives.
 - b. The Project Team determined that valve 765-12.36-2 had existing automation capabilities and did not require automation to achieve Valve Enhancement Plan objectives.
 - c. The Project Team determined that the automation of valve 765-12.36-4 was not necessary to achieve Valve Enhancement Plan objectives.
4. Final Project Scope: The final project scope consists of the automation of one MLV, that included the installation of one new actuator, the installation of one flowmeter, the installation of one new vault to house the flowmeter, and the installation of the necessary automation equipment.

Table 2: Final Project Scope

| Final Project Scope | | | | | |
|---------------------|--------|---------|---------------------------------------|----------------------|-----------|
| Line | Mile | Valve # | Valve Size (<i>confidential</i>) | Installation Type | Function |
| 765 | 12.36 | 0 | | A/AG | ASV/RCV |
| 2000 | 222.71 | FM | | FM | FLOWMETER |

B. Site Evaluation and Planning

SoCalGas initiated the planning process for the Spence Station Valve Enhancement Project by performing a pre-design site walk to determine the existing conditions and assess any potential impact on the design. Key factors that influenced the engineering and design of this project are as follows:

1. Site Description: The site is an existing SoCalGas facility in an industrial area north in the City of Los Angeles.
2. Land Issues: The Project Team did not anticipate any land issues for this project.

Final Report for Spence Station Valve Enhancement Project

3. DOT Class: This project site is in a Class 3 location.
4. Power Source: The project site had existing utility power.
5. Communication Technology: The project site had radio communications.

C. Engineering, Design, and Planning Factors

SoCalGas reviewed drawings and records, contacted internal planning groups, communicated with external stakeholders, conducted survey activity, performed potholing of the area to identify the presence of underground utilities and substructures, and completed a site walk. Key factors that influenced the engineering and design of the Project are as follows:


1. Engineering Assessment: During the site evaluation, the Project Team confirmed the existing technology and verified that the station could accommodate the new equipment.
2. Valve Details: The existing valve was a manually operated Class 300 ball valve, which was reused by the Project Team.
3. Actuator Details: There was no existing actuator. The Project Team installed a new actuator.
4. Customer Impact: The Project Team did not identify any anticipated service disruptions to customers.
5. Community Impact: The Project Team did not anticipate any notable impacts to the community during the project.
6. Substructures: The Project Team did not identify any existing substructures that affected the design and engineering at this site.
7. Environmental: The Project Team did not identify any notable environmental concerns at the site. An environmental monitor performed routine site visits during construction.
8. Permit Restrictions: There were no special permits or permit restrictions for this project.

Final Report for Spence Station Valve Enhancement Project

9. Land Use: The Project Team performed all work withing the existing SoCalGas facility.
10. Traffic Control: The Project Team did not identify any traffic control needs at the site.

Final Report for Spence Station Valve Enhancement Project

Figure 1: Spence Station Valve Enhancement Project Schematic

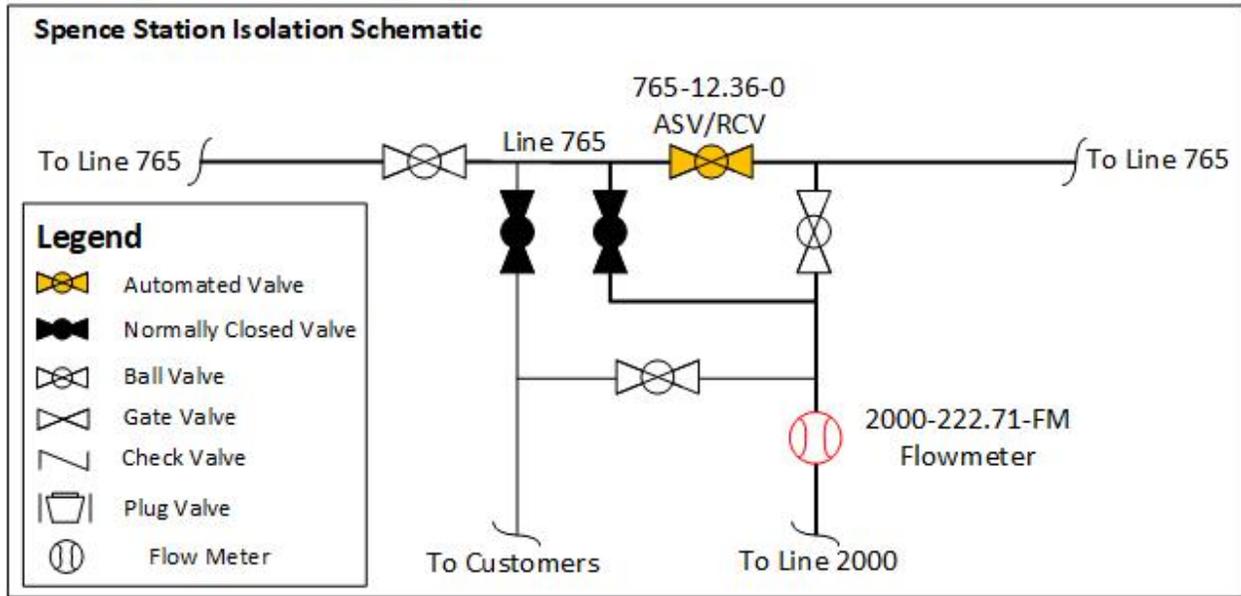

Final Report for Spence Station Valve Enhancement Project

D. Scope Changes

Through engineering, design, and planning activities, SoCalGas determined that a change in scope were appropriate to enhance the design of the Project and address engineering factors. As a result, the preliminary cost estimate does not fully reflect the final scope. A notable change in scope was made after the preliminary cost estimate was developed and approved. The Project Team determined that valve 765-12.36-4 did not require automation to achieve Valve Enhancement Plan objectives.

Final Report for Spence Station Valve Enhancement Project

III. CONSTRUCTION

A. Construction Contractor Selection

The Project Team prepared an initial cost estimate based on the preliminary design. Following completion of the engineering, design, and planning activities described above, the Project Team directed the Performance Partner (Mechanical Construction Contractor) and Alliance Partner (Electrical Contractor) to prepare cost estimates based on a more detailed engineering design package, which included the updated design described in the discussion of notable changes in scope above.

1. SoCalGas' Preliminary Mechanical Construction Contractor Estimate (confidential): SoCalGas' preliminary cost estimate for construction was [REDACTED].
2. Mechanical Construction Contractor's Target Price Estimate (confidential): The Mechanical Construction Contractor's cost estimate was [REDACTED], which was [REDACTED] than SoCalGas' preliminary cost estimate for construction.
3. SoCalGas' Preliminary Electrical Contractor Estimate (confidential): SoCalGas' preliminary cost estimate for construction was [REDACTED].
4. Electrical Contractor's Estimate (confidential): The Electrical Contractor's estimate was [REDACTED], which was [REDACTED] than SoCalGas' preliminary cost estimate.

Final Report for Spence Station Valve Enhancement Project

B. Construction Schedule

Table 3: Construction Timeline

| | |
|------------------------------|------------|
| Construction Start Date | 12/14/2017 |
| Construction Completion Date | 03/15/2018 |
| Days on Site | 36 days |
| Commissioning Date | 09/04/2019 |

The Project Team completed all construction activities as soon as practicable prior to commissioning. Finalization of commissioning activities is dependent on electrical utility connections, and system and/or resource availability.

C. Changes During Construction

SoCalGas successfully mitigated field conditions during construction in a manner that minimized potential impacts on project scope, cost, and schedule. As a result, these conditions did not result in any notable change orders.

Final Report for Spence Station Valve Enhancement Project

Figure 2: New Main Line Valve Actuator



Final Report for Spence Station Valve Enhancement Project

D. Commissioning and Site Restoration

Commissioning activities included site restoration, final inspections, and placement of the valve into service. During this stage, SoCalGas successfully performed site acceptance testing, and conducted point-to-point verification with SoCalGas Gas Control personnel for the newly-automated valve, and transferred ownership of the new equipment to Field Operations. Closeout activities included development of final drawings, the reconciliation package, and updates to company recordkeeping systems to reflect the completed scope of work. The site was commissioned on September 4, 2019, as summarized in Table 3.

Final Report for Spence Station Valve Enhancement Project

IV. PROJECT COSTS

A. Cost Avoidance Actions

SoCalGas exercised due diligence in the design, planning, and construction activities for this project to minimize or avoid costs when prudent to do so. As discussed above, the Project Team reviewed existing records, communicated with external stakeholders, and conducted a site walk to incorporate the site conditions in the project plan and design. The Project Team performed the work within a company facility.

B. Cost Estimates

Based on the preliminary design, once the preliminary project scope was confirmed and engineering, design, and planning activities were underway, SoCalGas prepared an estimate of the Direct Costs of the Project in the amount of \$1,525,219. The Project Team considered the conditions known at the time to prepare the preliminary Direct Cost estimate. This estimate reflects the projected Labor, Material, and Services costs anticipated to be incurred to execute the Project, based on initial design plans.

SoCalGas estimated Indirect Costs of the Project based on the estimated Direct Costs and other project-related variables.

C. Actual Direct and Indirect Costs

Actual Direct Costs reflect the Labor, Material, and Services costs incurred to execute the Project. Actual Indirect Costs reflect costs for incremental overhead loaders in accordance with Company overhead allocation policies. The total loaded cost of the Project is \$1,703,874.

Final Report for Spence Station Valve Enhancement Project

Table 4: Estimated and Actual Direct Costs and Variances²

| Direct Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|------------------------------------|------------------|------------------|--------------------|
| Company Labor | 317,827 | 180,424 | (137,403) |
| Materials | 173,400 | 169,015 | (4,385) |
| Mechanical Construction Contractor | 502,197 | 369,002 | (133,195) |
| Electrical Contractor | 113,043 | 127,332 | 14,289 |
| Construction Management & Support | 65,486 | 112,426 | 46,940 |
| Environmental | 67,163 | 19,413 | (47,750) |
| Engineering & Design | 72,078 | 132,868 | 60,790 |
| Project Management & Services | 55,634 | 19,608 | (36,027) |
| ROW & Permits | - | 436 | 436 |
| GMA | 158,391 | 178,750 | 20,359 |
| Total Direct Costs | 1,525,219 | 1,309,272 | (215,947) |

Table 5: Estimated and Actual Indirect Costs, Total Costs, and Variances³

| Indirect Costs/Total Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|---------------------------------|------------------|------------------|--------------------|
| Overheads | 357,274 | 249,507 | (107,767) |
| AFUDC | 84,073 | 126,370 | 42,297 |
| Property Taxes | 19,695 | 18,725 | (970) |
| Total Indirect Costs | 461,042 | 394,602 | (66,440) |
| Total Direct Costs | 1,525,219 | 1,309,272 | (215,947) |
| Total Loaded Costs | 1,986,261 | 1,703,874 | (282,387) |

² Values may not add to total due to rounding.

³ Ibid.

Final Report for Spence Station Valve Enhancement Project

V. CONCLUSION

SoCalGas enhanced the safety of their integrated natural gas system by prudently executing the Spence Station Valve Enhancement Project. Through this Valve Enhancement Project, SoCalGas successfully automated one mainline valve on Line 765 and installed a flowmeter on Line 2000 to achieve the objective of enabling rapid system isolation to a portion of Line 765 in the City of Los Angeles. The total loaded cost of the Project is \$1,703,874.

SoCalGas executed this project prudently through designing and executing the project to support achievement of Valve Enhancement Plan isolation objectives, installing the necessary automation equipment, and installing equipment necessary to bring communication capabilities to the site to enable rapid system isolation of a portion of Line 765 located in the urban area north of the Los Angeles River in the City of Los Angeles.

SoCalGas engaged in prudent cost avoidance efforts to complete this safety enhancement at a reasonable cost by carefully planning and coordinating engineering and construction activities to maximize efficiencies and reduce customer and community impacts, engaging in reasonable efforts to promote competitive and market-based rates for contractor services and materials, and using a reasonable amount of company and contractor resources to complete this safety enhancement as soon as practicable.

End of Spence Station Valve Enhancement Project Final Report

Final Report for Taft Valve Enhancement Project – 7th Standard

I. TAFT VALVE ENHANCEMENT PROJECT – 7TH STANDARD

A. Background and Summary

The Taft Valve Enhancement Project – 7th Standard site consists of valve enhancements made to an existing mainline valve (MLV) located in Kern County. Through this project, SoCalGas enhanced the safety of its natural gas transmission system by enabling the rapid detection of a significant change in pipeline pressure and remote isolation and depressurization of a portion of Line 7039 in the event of a pipeline rupture. SoCalGas installed a new actuator, new fencing, new power equipment, new communications equipment, and the necessary automation equipment at the site. The total loaded project cost is \$1,356,740.

The Taft Valve Enhancement Project – 7th Standard construction site is within an existing SoCalGas facility in an open area next to an irrigation canal. There are multiple industrial facilities nearby. SoCalGas bundled this valve project with three additional valve projects, Taft Valve Enhancement Projects – Buttonwillow; Hageman and Renfro; and Sycamore Road, into a single valve bundle to gain efficiencies in engineering, planning, and construction activities. This workpaper describes the construction activities and costs of the Line 225 Valve Enhancement Project – 7th Standard site.

Final Report for Taft Valve Enhancement Project – 7th Standard

Table 1: General Project Information

| Taft Valve Enhancement Project – 7th Standard | | | |
|--|-----------------|----------------|--------------|
| Location | Kern County | | |
| Days on Site | 37 days | | |
| Construction Start | 09/11/2017 | | |
| Construction Finish | 11/29/2017 | | |
| Commissioning Date | 08/22/2018 | | |
| Valve Upgrades | | | |
| Valve Number | 7039-11.49-0 | | |
| Valve Type | Existing – Ball | | |
| Actuator | New | | |
| Actuator Above-/Below-Grade | Above-Grade | | |
| ASV | Yes | | |
| RCV | Yes | | |
| Site Upgrades | | | |
| Vault | None | | |
| Power | New – Utility | | |
| Communication | New – Radio | | |
| SCADA Panel | New | | |
| Equipment Shelter | New | | |
| Fencing | New | | |
| Project Costs (\$) | Capital | O&M | Total |
| Loaded Project Costs | 1,356,740 | 0 | 1,356,740 |
| Disallowed Costs | 0 | 0 | 0 |

Final Report for Taft Valve Enhancement Project – 7th Standard

B. Maps and Images

Figure 1: Taft Bundle Overview



Final Report for Taft Valve Enhancement Project – 7th Standard

Figure 2: Satellite Image of Taft Valve Enhancement Project – 7th Standard



Final Report for Taft Valve Enhancement Project – 7th Standard

II. ENGINEERING, DESIGN, AND PLANNING

A. Project Scope

SoCalGas presented a conceptual project scope for the Taft Valve Enhancement Project – 7th Standard in workpapers supporting the Valve Enhancement Plan in the 2011 PSEP filing.¹ This conceptual scope identified MLV 7039-11.49-0 for automation to enable remote isolation to a portion of Line 7039. Prior to initiating execution of the Project, SoCalGas reviewed available information and performed a detailed system flow analysis to validate the scope of the Project, and confirmed that this enhancement will provide the planned isolation. The final project scope is summarized in Table 2 below.

1. 2011 PSEP Filing: SoCalGas identified MLV 7039-11.49-0 for automation to achieve the objective of rapid system isolation.
2. Updated Scope: Upon project initiation, SoCalGas reviewed the conceptual project scope and determined that this isolation point would achieve the transmission isolation objectives set forth in the Valve Enhancement Plan.
3. Engineering, Design, and Constructability: The Project Team initially planned to install a new actuator in a new vault. During the site evaluation, the Project Team determined that the new actuator could be installed above grade and the new vault was not necessary.
4. Final Project Scope: The final project scope consists of the automation of one MLV that included the installation of a new actuator, the installation of new fencing, the installation of new power equipment, the installation of new communications equipment, and the installation of the necessary automation equipment at the site.

¹ See Workpapers supporting Amended Pipeline Safety Enhancement Plan (PSEP) of SoCalGas and SDG&E, submitted on December 2, 2011, at WP-IX-2-14 through WP-IX-2-25 (A.11-11-002 Exh. SCG-32).

Final Report for Taft Valve Enhancement Project – 7th Standard

Table 2: Final Project Scope

| Final Project Scope | | | | | |
|---------------------|-------|---------|---------------------------------------|----------------------|----------|
| Line | Mile | Valve # | Valve Size (<i>confidential</i>) | Installation Type | Function |
| 7039 | 11.49 | 0 | | A/AG | ASV/RCV |

B. Site Evaluation and Planning

SoCalGas initiated the planning process for the Taft Valve Enhancement Project – 7th Standard by performing a pre-design site walk to determine the existing conditions and assess any potential impact on the design. Key factors that influenced the engineering and design of this project are as follows:

1. Site Description: The site is an existing SoCalGas facility in an open area next to an irrigation canal. There are multiple industrial facilities nearby.
2. Land Issues: During the pre-design site walk, the Project Team noted that the existing stations would need to be expanded to accommodate the additional equipment.
3. DOT Class: This project site is in a Class 3 location.
4. Power Source: There was no preexisting power source. The Project Team installed new power equipment at the site.
5. Communication Technology: There was no preexisting communications equipment. The Project Team installed new communications equipment at the site.

C. Engineering, Design, and Planning Factors


SoCalGas reviewed drawings and records, contacted internal planning groups, communicated with external stakeholders, conducted survey activity, and completed a site walk. Key factors that influenced the engineering and design of the Project are as follows:

Final Report for Taft Valve Enhancement Project – 7th Standard

1. Engineering Assessment: During the site evaluation the Project Team confirmed the existing technology and verified the need to expand the existing station to accommodate the new equipment.
2. Valve Details: The existing valve was a manually operated Class 600 ball, which was reused by the Project Team.
3. Actuator Details: There was no preexisting actuator so the Project Team installed a new actuator.
4. Customer Impact: The Project Team did not identify any anticipated service disruptions to customers.
5. Community Impact: The Project Team did not anticipate any notable impact to the community from this Project.
6. Substructures: The Project Team did not identify any existing substructures that affected the design and engineering at this site.
7. Environmental: The Project Team did not identify any notable environmental concerns at the site. An environmental monitor performed routine site visits during construction.
8. Permit Restrictions: There were no special permits or permit restrictions for this project.
9. Land Use: The Project Team entered into a license agreement with the North Kern Water Storage District for the land necessary to expand the existing facility. The Project Team also obtained a Temporary Right of Entry for the duration of construction.
10. Traffic Control: The Project Team did not identify any traffic control needs at the site.

Final Report for Taft Valve Enhancement Project – 7th Standard

Figure 3: Taft Valve Enhancement Project – 7th Standard Schematic

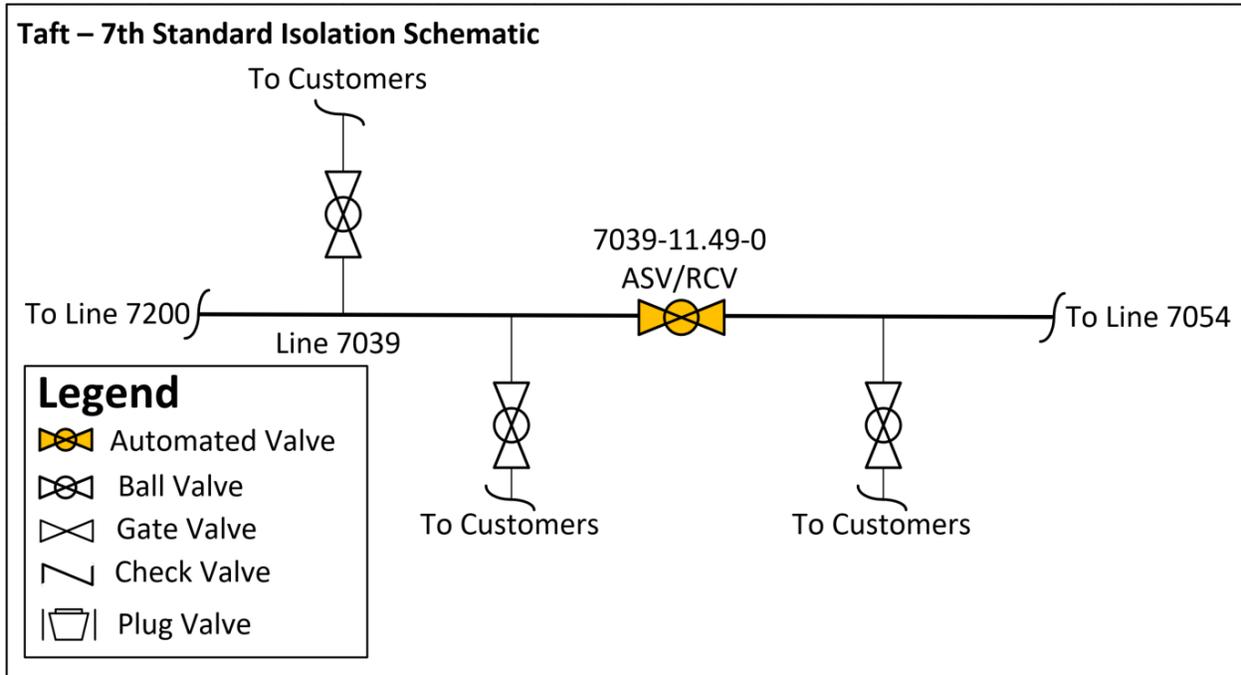

Final Report for Taft Valve Enhancement Project – 7th Standard

D. Scope Changes

Through engineering, design, and planning activities, SoCalGas determined that changes in scope were appropriate to enhance the design of the Project and address engineering factors. As a result, the preliminary cost estimate does not fully reflect the final scope. A notable change in scope was made after the preliminary cost estimate was developed and approved. The Project Team initially planned to install a ground grid at the new station. After the creation of the Stage 3 Estimate, the Project Team determined that the ground grid was not necessary.

Final Report for Taft Valve Enhancement Project – 7th Standard

III. CONSTRUCTION

A. Construction Contractor Selection

The Project Team prepared an initial cost estimate based on the preliminary design. Following completion of the engineering, design, and planning activities described above, the Project Team directed the Performance Partner (Mechanical Construction Contractor) and Alliance Partner (Electrical Contractor) to prepare cost estimates based on a more detailed engineering design package, which included the updated design described in the discussion of notable changes in scope above.

1. SoCalGas' Preliminary Mechanical Construction Contractor Estimate (*confidential*): SoCalGas' preliminary cost estimate for construction was [REDACTED].
2. Mechanical Construction Contractor's Target Price Estimate (*confidential*): The Mechanical Construction Contractor's cost estimate was [REDACTED], which was [REDACTED] than SoCalGas' preliminary cost estimate for construction.
3. SoCalGas' Preliminary Electrical Contractor Estimate (*confidential*): SoCalGas' preliminary cost estimate for the electrical contractor was [REDACTED].
4. Electrical Contractor's Estimate (*confidential*): The Electrical Contractor's estimate was [REDACTED], which was [REDACTED] than SoCalGas' preliminary cost estimate.

Final Report for Taft Valve Enhancement Project – 7th Standard

B. Construction Schedule

Table 3: Construction Timeline

| | |
|------------------------------|------------|
| Construction Start Date | 09/11/2017 |
| Construction Completion Date | 11/29/2017 |
| Days on Site | 37 days |
| Commissioning Date | 08/22/2018 |

The Project Team completed all construction activities as soon as practicable prior to commissioning. Finalization of commissioning activities is dependent on electrical utility connections, and system and/or resource availability.

C. Changes During Construction

SoCalGas successfully mitigated field conditions during construction in a manner that minimized potential impacts on project scope, cost, and schedule. As a result, these conditions did not result in any notable change orders.

Final Report for Taft Valve Enhancement Project – 7th Standard

Figure 4: Setup for Instrument Piping Pressure Test



Final Report for Taft Valve Enhancement Project – 7th Standard

D. Commissioning and Site Restoration

Commissioning activities included site restoration, final inspections, and placement of the valve into service. During this stage, SoCalGas successfully performed site acceptance testing and conducted point-to-point verification with Gas Control personnel for the newly-automated valve, and transferred ownership of the new equipment to Field Operations. Closeout activities included development of final drawings, the reconciliation package, and updates to company recordkeeping systems to reflect the completed scope of work. The site was commissioned on August 22, 2018, as summarized in Table 3.

Final Report for Taft Valve Enhancement Project – 7th Standard

IV. PROJECT COSTS

A. Cost Avoidance Actions

SoCalGas exercised due diligence in the design, planning, and construction activities for this project to minimize or avoid costs when prudent to do so. As discussed above, the Project Team reviewed existing records, communicated with external stakeholders, and conducted a site walk to incorporate the site conditions in the project plan and design. The Project Team bundled this project with the Taft Valve Enhancement Projects – Buttonwillow, Hageman and Renfro, and Sycamore Road, coordinating engineering and construction activities between the project sites to minimize costs for the benefit of the customers.

B. Cost Estimates

Based on the preliminary design, once the preliminary project scope was confirmed and engineering, design, and planning activities were underway, SoCalGas prepared an estimate of the Direct Costs of the Project in the amount of \$1,483,999. The Project Team considered the conditions known at the time to prepare the preliminary Direct Cost estimate. This estimate reflects the projected Labor, Material, and Services costs anticipated to be incurred to execute the Project, based on initial design plans.

SoCalGas estimated Indirect Costs of the Project based on the estimated Direct Costs and other project-related variables.

C. Actual Direct and Indirect Costs

Actual Direct Costs reflect the Labor, Material, and Services costs incurred to execute the Project. Actual Indirect Costs reflect costs for incremental overhead loaders in accordance with Company overhead allocation policies. The total loaded cost of the Project is \$1,356,740.

Final Report for Taft Valve Enhancement Project – 7th Standard

Table 4: Estimated and Actual Direct Costs and Variances²

| Direct Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|------------------------------------|------------------|------------------|--------------------|
| Company Labor | 189,750 | 69,844 | (119,906) |
| Materials | 138,133 | 83,115 | (55,018) |
| Mechanical Construction Contractor | 394,123 | 271,273 | (122,850) |
| Electrical Contractor | 172,628 | 109,336 | (63,292) |
| Construction Management & Support | 71,170 | 111,115 | 39,945 |
| Environmental | 63,635 | 66,820 | 3,185 |
| Engineering & Design | 178,648 | 232,529 | 53,881 |
| Project Management & Services | 132,753 | 45,582 | (87,171) |
| ROW & Permits | 8,250 | 23,193 | 14,943 |
| GMA | 134,909 | 142,090 | 7,181 |
| Total Direct Costs | 1,483,999 | 1,154,898 | (329,101) |

Table 5: Estimated and Actual Indirect Costs, Total Costs, and Variances³

| Indirect Costs/Total Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|---------------------------------|------------------|------------------|--------------------|
| Overheads | 221,978 | 139,299 | (82,679) |
| AFUDC | 102,974 | 54,192 | (48,782) |
| Property Taxes | 24,566 | 8,350 | (16,216) |
| Total Indirect Costs | 349,518 | 201,842 | (147,676) |
| Total Direct Costs | 1,483,999 | 1,154,898 | (329,101) |
| Total Loaded Costs | 1,833,519 | 1,356,740 | (476,779) |

² Values may not add to total due to rounding.

³ Ibid.

Final Report for Taft Valve Enhancement Project – 7th Standard

V. CONCLUSION

SoCalGas enhanced the safety of its natural gas system by prudently executing the Taft Valve Enhancement Project - 7th Standard. Through this Valve Enhancement Project, SoCalGas successfully automated one mainline valve to achieve the objective of enabling rapid system isolation to a portion of Line 7039 located within Kern County. The total loaded cost of the Project is \$1,356,740.

SoCalGas executed this project prudently through: designing and executing the project to support achievement of Valve Enhancement Plan isolation objectives, bundling four geographically proximate projects together to capture efficiencies through coordinated engineering and construction planning, and installing equipment necessary to bring power and communication capabilities to the site to enable rapid system isolation to a portion of Line 7039 located within Kern County.

SoCalGas engaged in prudent cost avoidance efforts to complete this safety enhancement at a reasonable cost by carefully planning and coordinating engineering and construction activities to maximize efficiencies and reduce customer and community impacts.

End of Taft Valve Enhancement Project – 7th Standard Final Report

Final Report for Taft Valve Enhancement Project - Buttonwillow

I. TAFT VALVE ENHANCEMENT PROJECT – BUTTONWILLOW

A. Background and Summary

The Taft Valve Enhancement Project – Buttonwillow consists of valve enhancements made to one existing mainline valve (MLV) located in the unincorporated community of Buttonwillow within Kern County. Through this project SoCalGas enhanced the safety of its natural gas transmission system by enabling the rapid detection of a significant change in pipeline pressure and remote isolation and depressurization of a portion of Line 293 in the event of a pipeline rupture. SoCalGas installed a new actuator, new power equipment, new communications equipment, new fencing, and the necessary automation equipment at the site. The total loaded project cost is \$1,419,326.

The Taft Valve Enhancement Project – Buttonwillow construction site is within an existing SoCalGas facility on Highway 58 in a farmland area. SoCalGas bundled this valve project with three additional valve projects, the Taft Valve Enhancement Projects – 7th Standard, Hageman and Renfro, and Sycamore Road, into a single valve bundle to gain efficiencies in engineering, planning, and construction activities. The Project Team tracked the projects separately to more effectively track cost and streamline project closeout for individual sites. This workpaper describes the construction activities and costs of the Taft Valve Enhancement Project – Buttonwillow.

Final Report for Taft Valve Enhancement Project - Buttonwillow

Table 1: General Project Information

| Taft Valve Enhancement Project - Buttonwillow | | | |
|--|-----------------|----------------|--------------|
| Location | Buttonwillow | | |
| Days on Site | 46 days | | |
| Construction Start | 04/03/2017 | | |
| Construction Finish | 07/06/2017 | | |
| Commissioning Date | 03/28/2018 | | |
| Valve Upgrades | | | |
| Valve Number | 293-8.23-0 | | |
| Valve Type | Existing – Ball | | |
| Actuator | New | | |
| Actuator Above-/Below-Grade | Above-Grade | | |
| ASV | Yes | | |
| RCV | Yes | | |
| Site Upgrades | | | |
| Vault | None | | |
| Power | New – Solar | | |
| Communication | New – Radio | | |
| SCADA Panel | New | | |
| Equipment Shelter | None | | |
| Fencing | Yes | | |
| Project Costs (\$) | Capital | O&M | Total |
| Loaded Project Costs | 1,419,326 | 0 | 1,419,326 |
| Disallowed Costs | 0 | 0 | 0 |

Final Report for Taft Valve Enhancement Project - Buttonwillow

B. Maps and Images

Figure 1: Taft Bundle Overview



Final Report for Taft Valve Enhancement Project - Buttonwillow

Figure 2: Satellite Image of Taft Valve Enhancement Project - Buttonwillow



Final Report for Taft Valve Enhancement Project - Buttonwillow

II. ENGINEERING, DESIGN, AND PLANNING

A. Project Scope

SoCalGas presented a conceptual project scope for the Taft Valve Enhancement Project – Buttonwillow in workpapers supporting the Valve Enhancement Plan in the 2011 PSEP filing.¹ This conceptual scope identified MLV 293-8.23-0, for automation to enable remote isolation to a portion of Line 293. Prior to initiating execution of the Project, SoCalGas reviewed available information, performed a detailed system flow analysis to validate the scope of the Project, and confirmed that this enhancement will provide the planned isolation. The final project scope is summarized in Table 2 below.

1. 2011 PSEP Filing: SoCalGas identified MLVs 293-8.23-0 for automation to achieve the objective of rapid system isolation.
2. Updated Scope: Upon project initiation, SoCalGas reviewed the conceptual project scope and determined that this isolation point would achieve the transmission isolation objectives set forth in the Valve Enhancement Plan.
3. Engineering, Design, and Constructability: No notable engineering adjustments were required to the standard design.
4. Final Project Scope: The final project scope consists of the automation of one MLV, that includes the installation of one new actuator, the installation of new fencing, the installation of power equipment, the installation of communications equipment, and the installation of the necessary automation equipment at the site.

¹ See Workpapers supporting Amended Pipeline Safety Enhancement Plan (PSEP) of SoCalGas and SDG&E, submitted on December 2, 2011, at WP-IX-2-14 through WP-IX-2-25 (A.11-11-002 Exh. SCG-32).

Final Report for Taft Valve Enhancement Project - Buttonwillow

Table 2: Final Project Scope

| Final Project Scope | | | | | |
|---------------------|------|---------|---------------------------------------|----------------------|----------|
| Line | Mile | Valve # | Valve Size (<i>confidential</i>) | Installation Type | Function |
| 293 | 8.23 | 0 | | A/AG | ASV/RCV |

B. Site Evaluation and Planning

SoCalGas initiated the planning process for the Taft Valve Enhancement Project – Buttonwillow by performing a pre-design site walk to determine the existing conditions and assess any potential impact on the design. Key factors that influenced the engineering and design of this project are as follows:

1. Site Description: The site is located in a fenced in station north of Highway 58 in a farmland area.
2. Land Issues: During the pre-design site walk, the Project Team noted that the existing station would need to be expanded to accommodate the additional equipment.
3. DOT Class: This project site is in a Class 1 location. SoCalGas selected this MLV for automation to satisfy the objectives of the PSEP Valve Enhancement Plan.
4. Power Source: There was no preexisting power source. The Project Team installed new power equipment at the site.
5. Communication Technology: There was no preexisting communications equipment. The Project Team installed new communications equipment at the site.

C. Engineering, Design, and Planning Factors


SoCalGas reviewed drawings and records, contacted internal planning groups, communicated with external stakeholders, conducted survey activity, and completed a site walk. Key factors that influenced the engineering and design of the Project are as follows:

Final Report for Taft Valve Enhancement Project - Buttonwillow

1. Engineering Assessment: During the site evaluation the Project Team confirmed the existing technology and verified the need to expand the existing station to accommodate the new equipment.
2. Valve Details: The existing valve was a manually operated Class 600 ball valve, which was reused by the Project Team.
3. Actuator Details: There was no preexisting actuator. The Project Team installed a new actuator.
4. Customer Impact: The Project Team did not identify any anticipated service disruptions to customers.
5. Community Impact: The Project Team did not anticipate any notable impact to the community from this Project.
6. Substructures: The Project Team did not identify any existing substructures that affected the design and engineering at this site.
7. Environmental: The Project Team did not identify any notable environmental concerns at the site. An environmental monitor performed routine site visits during construction.
8. Permit Restrictions: There were no special permits or permit restrictions for this project site.
9. Land Use: The Project Team obtained a new easement for the expansion of the existing SoCalGas facility. The Project Team also obtained a Temporary Right of Entry for construction. The Project Team utilized the area around the facility as a laydown yard.
10. Traffic Control: The Project Team placed cones along Highway 58 during construction.

Final Report for Taft Valve Enhancement Project - Buttonwillow

Figure 3: Taft Valve Enhancement Project – Buttonwillow Schematic

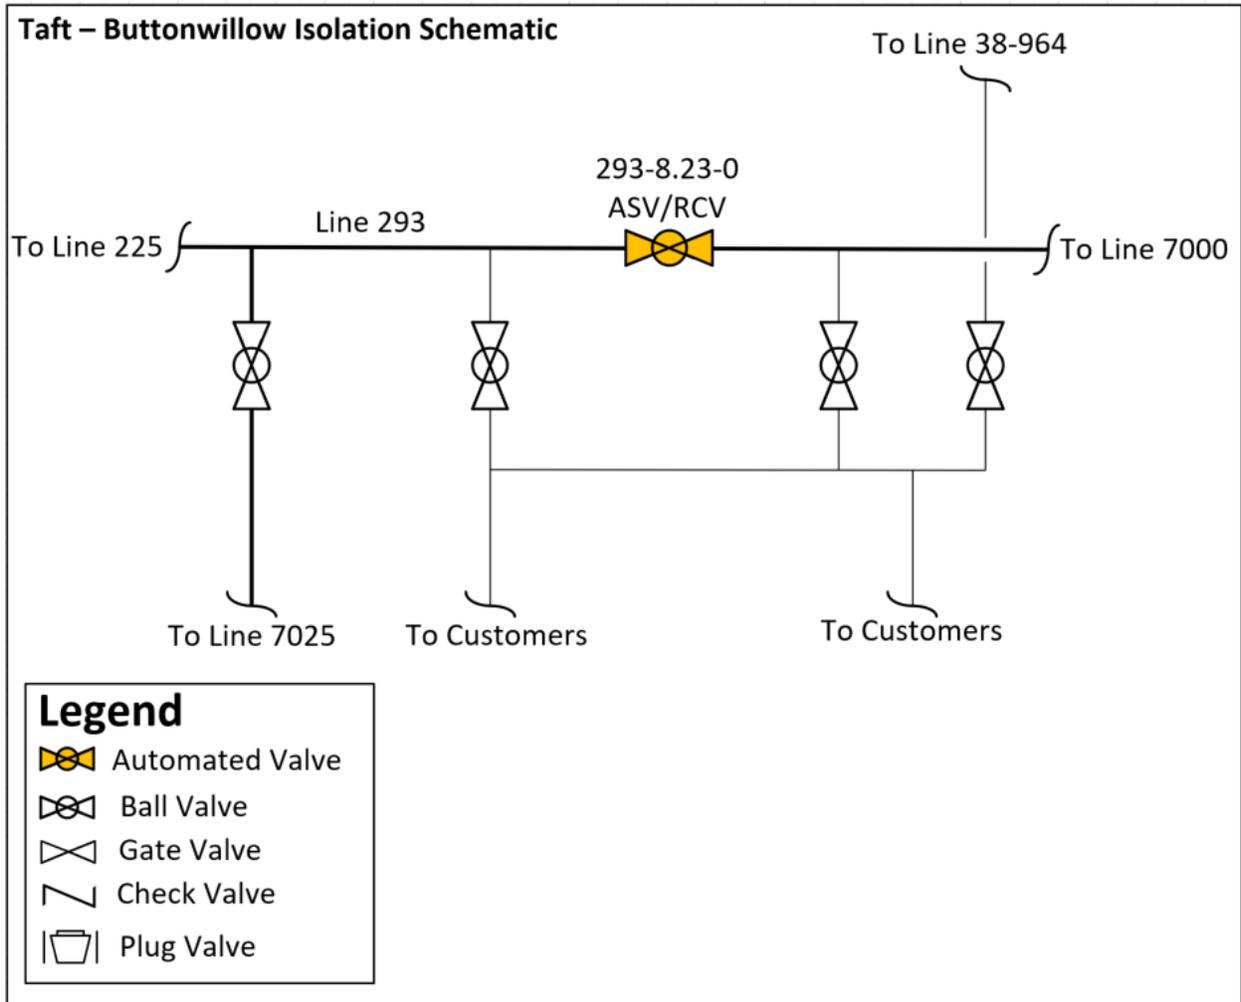

Final Report for Taft Valve Enhancement Project - Buttonwillow

D. Scope Changes

SoCalGas did not make any notable scope changes during detailed design.

Final Report for Taft Valve Enhancement Project - Buttonwillow

III. CONSTRUCTION

A. Construction Contractor Selection

The Project Team prepared an initial cost estimate based on the preliminary design. Following completion of the engineering, design, and planning activities described above, the Project Team directed the Performance Partner (Mechanical Construction Contractor) and Alliance Partner (Electrical Contractor) to prepare cost estimates based on a more detailed engineering design package. As indicated above, there were no notable changes in scope between the time when the Project Team prepared the preliminary cost estimate and when the Performance Partner and Alliance Partner prepared and submitted their estimates.

1. SoCalGas' Preliminary Mechanical Construction Contractor Estimate (*confidential*): SoCalGas' preliminary cost estimate for construction was [REDACTED].
2. Mechanical Construction Contractor's Target Price Estimate (*confidential*): The Mechanical Construction Contractor's cost estimate was [REDACTED]1, which was [REDACTED] than SoCalGas' preliminary cost estimate for construction.
3. SoCalGas' Preliminary Electrical Contractor Estimate (*confidential*): SoCalGas' preliminary cost estimate for construction was [REDACTED].
4. Electrical Contractor's Estimate (*confidential*): The Electrical Contractor's estimate was [REDACTED], which was [REDACTED] than SoCalGas' preliminary cost estimate.

Final Report for Taft Valve Enhancement Project - Buttonwillow

B. Construction Schedule

Table 3: Construction Timeline

| | |
|------------------------------|------------|
| Construction Start Date | 04/03/2017 |
| Construction Completion Date | 07/06/2017 |
| Days on Site | 46 days |
| Commissioning Date | 03/28/2018 |

The Project Team completed all construction activities as soon as practicable prior to commissioning. Finalization of commissioning activities is dependent on electrical utility connections, and system and/or resource availability.

C. Changes During Construction

The conditions summarized below were encountered during construction. Activities to address or mitigate these conditions resulted in approximately \$36,000 in change orders.

1. Extended Scope: The Project Team expanded a portion of the station to accommodate the necessary communications equipment. The new portion of fencing was higher than the remaining portions. The Project Team replaced the existing fencing so that the station fencing was uniform and improved the station's security.
2. Field Design Change: The Project Team installed solar power rather than connecting to the local utility after the utility informed the Project Team that the existing pole could not accommodate the new power equipment and required siting the new pole on the opposite side of the highway. To avoid the costs of permitting, trenching, and boring under the highway, the Project Team chose the more cost efficient option of solar power.

Final Report for Taft Valve Enhancement Project - Buttonwillow

Figure 4: Excavation Around Valve Assembly and New Actuator



Final Report for Taft Valve Enhancement Project - Buttonwillow

D. Commissioning and Site Restoration

Commissioning activities included site restoration, final inspections, and placement of the valve into service. During this stage, SoCalGas successfully performed site acceptance testing and conducted point-to-point verification with Gas Control personnel for the newly-automated valve, and transferred ownership of the new equipment to Field Operations. Closeout activities included development of final drawings, the reconciliation package, and updates to company recordkeeping systems to reflect the completed scope of work. The site was commissioned on March 28, 2018, as summarized in Table 3.

Final Report for Taft Valve Enhancement Project - Buttonwillow

IV. PROJECT COSTS

A. Cost Avoidance Actions

SoCalGas exercised due diligence in the design, planning, and construction activities for this project to minimize or avoid costs when prudent to do so. As discussed above, the Project Team reviewed existing records, communicated with external stakeholders, and conducted a site walk to incorporate known site conditions in the project plan and design.

1. Project Design: The Project Team altered the project design to utilize solar power instead of utility power. Installing utility power would have resulted in increased permitting costs as well as project delays.
2. Bundling of Projects: The Project Team bundled this project with the Taft Valve Enhancement Projects – 7th Standard, Hageman and Renfro, and Sycamore Road, coordinating engineering and construction activities between the project sites to minimize costs for the benefit of the customers.

B. Cost Estimates

Based on the preliminary design, once the preliminary project scope was confirmed and engineering, design, and planning activities were underway, SoCalGas prepared an estimate of the Direct Costs of the Project in the amount of \$1,441,658. The Project Team considered the conditions known at the time to prepare the preliminary Direct Cost estimate. This estimate reflects the projected Labor, Material, and Services costs anticipated to be incurred to execute the Project, based on initial design plans.

SoCalGas estimated Indirect Costs of the Project based on the estimated Direct Costs and other project-related variables.

Final Report for Taft Valve Enhancement Project - Buttonwillow

C. Actual Direct and Indirect Costs

Actual Direct Costs reflect the Labor, Material, and Services costs incurred to execute the Project. Actual Indirect Costs reflect costs for incremental overhead loaders in accordance with Company overhead allocation policies. The total loaded cost of the Project is \$1,419,326.

Table 4: Estimated and Actual Direct Costs and Variances²

| Direct Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|------------------------------------|------------------|------------------|--------------------|
| Company Labor | 189,750 | 73,138 | (116,612) |
| Materials | 115,423 | 94,046 | (21,377) |
| Mechanical Construction Contractor | 455,509 | 321,778 | (133,731) |
| Electrical Contractor | 119,800 | 107,153 | (12,647) |
| Construction Management & Support | 71,170 | 104,110 | 32,940 |
| Environmental | 41,635 | 79,121 | 37,486 |
| Engineering & Design | 178,507 | 255,612 | 77,105 |
| Project Management & Services | 132,753 | 39,327 | (93,426) |
| ROW & Permits | 6,050 | 17,265 | 11,215 |
| GMA | 131,060 | 141,984 | 10,924 |
| Total Direct Costs | 1,441,658 | 1,233,534 | (208,124) |

Table 5: Estimated and Actual Indirect Costs, Total Costs, and Variances³

| Indirect Costs/Total Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|---------------------------------|------------------|------------------|--------------------|
| Overheads | 220,956 | 115,623 | (105,333) |
| AFUDC | 67,513 | 61,793 | (5,720) |
| Property Taxes | 15,961 | 8,375 | (7,586) |
| Total Indirect Costs | 304,430 | 185,792 | (118,638) |
| Total Direct Costs | 1,441,658 | 1,233,534 | (208,123) |
| Total Loaded Costs | 1,746,088 | 1,419,326 | (326,762) |

² Values may not add to total due to rounding.

³ Ibid.

Final Report for Taft Valve Enhancement Project - Buttonwillow

V. CONCLUSION

SoCalGas enhanced the safety of its natural gas system by prudently executing the Taft Valve Enhancement Project – Buttonwillow site. Through this Valve Enhancement Project, SoCalGas successfully automated one existing mainline valve to achieve the objective of enabling rapid system isolation of a portion of Line 293 located in the unincorporated community of Buttonwillow within Kern County. The total loaded cost of the Project is \$1,419,326.

SoCalGas executed this project prudently through: designing and executing the project to support achievement of Valve Enhancement Plan isolation objectives, bundling four geography proximate projects together to capture efficiencies through coordinated engineering and construction planning, and installing equipment necessary to bring power and communication capabilities to the site to enable rapid system isolation to a portion of Line 293 located in the unincorporated community of Buttonwillow within Kern County.

SoCalGas engaged in prudent cost avoidance efforts to complete this safety enhancement at a reasonable cost by installing solar power at the project site instead of utility power reducing overall project costs, by limiting the number of mobilizations by carefully planning and coordinating construction activity, and by carefully planning and coordinating engineering and construction activities to maximize efficiencies and reduce customer and community impacts.

End of Taft Valve Enhancement Project – Buttonwillow Final Report

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

I. TAFT VALVE ENHANCEMENT PROJECT - HAGEMAN AND RENFRO

A. Background and Summary

The Taft Valve Enhancement Project - Hageman and Renfro consists of valve enhancements made to two new mainline valves (MLVs) located in the City of Bakersfield within Kern County. Through this project, SoCalGas enhanced the safety of its natural gas transmission system by enabling the rapid detection of a significant change in pipeline pressure and remote isolation and depressurization of a portion of Line 7039 and Supply Line 38-7030 in the event of a pipeline rupture. SoCalGas removed one MLV, installed two new valves, two new actuators, two new vaults to house the actuators, new power equipment, new communications equipment, and the necessary automation equipment at the sites. The total loaded project cost is \$8,150,072.

The Taft Valve Enhancement Project - Hageman and Renfro Project consists of two construction sites. The first construction site, MLV 38-7030-1 is located on Hageman Road in the City of Bakersfield. The second construction site, MLV 7039-5.14-0 is located on Renfro Road in the City of Bakersfield approximately half a mile north of the first site. Both sites are located in residential areas with the MLV 7039-5.14-0 site adjacent to an agricultural field. SoCalGas bundled these two sites into one into a single valve bundle to gain efficiencies in engineering, planning and construction activities.

Final Report for Taft Valve Enhancement Project - Hageman and Renfro


Table 1: General Project Information

| Taft Valve Enhancement Project - Hageman and Renfro | | | |
|--|---------------------|----------------|--------------|
| Location | City of Bakersfield | | |
| Days on Site | 88 days | | |
| Construction Start | 11/09/2018 | | |
| Construction Finish | 04/25/2019 | | |
| Commissioning Date | 10/17/2019 | | |
| Valve Upgrades | | | |
| Valve Number | 38-7030-1 | | |
| Valve Type | New – Ball | | |
| Actuator | New | | |
| Actuator Above-/Below-Grade | Below-Grade | | |
| ASV | No | | |
| RCV | Yes | | |
| Valve Number | 7039-5.14-0 | | |
| Valve Type | New – Ball | | |
| Actuator | New | | |
| Actuator Above-/Below-Grade | Below-Grade | | |
| ASV | Yes | | |
| RCV | Yes | | |
| Site Upgrades | | | |
| Vault | New – Two | | |
| Power | New – Utility | | |
| Communication | New – Radio | | |
| SCADA Panel | New | | |
| Equipment Shelter | None | | |
| Fencing/Wall | None | | |
| Project Costs (\$) | Capital | O&M | Total |
| Loaded Project Costs | 8,150,072 | - | 8,150,072 |
| Disallowed Costs | - | - | - |

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

B. Maps and Images

Figure 1: Satellite Image of Taft Valve Enhancement Project - Hageman and Renfro

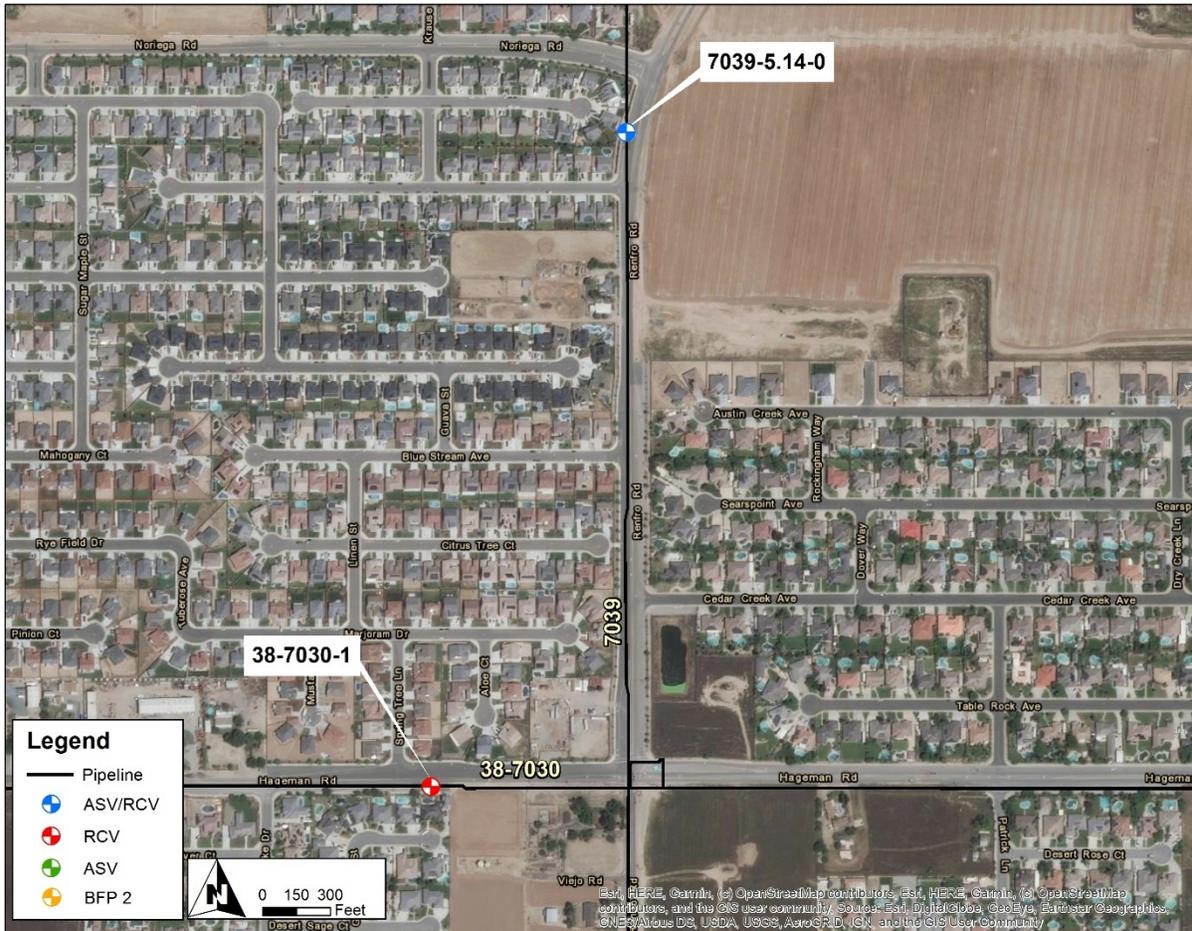

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

Figure 2: Satellite Image of Taft Valve Enhancement Project - Hageman Road



Final Report for Taft Valve Enhancement Project - Hageman and Renfro

Figure 3: Satellite Image of Taft Valve Enhancement Project - Renfro Road



Final Report for Taft Valve Enhancement Project - Hageman and Renfro

II. ENGINEERING, DESIGN, AND PLANNING

A. Project Scope

SoCalGas and SDG&E presented a conceptual project scope for the Taft Valve Enhancement Project – Hageman and Renfro in workpapers supporting the Valve Enhancement Plan in the 2011 PSEP filing¹. This conceptual scope identified MLV 7039-4.69-0 for automation to enable remote isolation to a portion of Line 7039. Prior to initiating execution of the Project, SoCalGas reviewed available information and performed a detailed system flow analysis to validate the scope of the Project, and confirmed that this valve enhancement will provide the planned isolation. The final project scope is summarized in Table 2 below.

1. 2011 PSEP Filing: SoCalGas identified MLV 7039-4.69-0 for automation to achieve the objective of rapid system isolation.
2. Updated Scope: Upon project initiation, SoCalGas reviewed the conceptual project scope and determined that this isolation point would enable rapid isolation, thereby achieving Valve Enhancement Plan objectives.
3. Engineering, Design, and Constructability: SoCalGas initially planned to automate MLV 7039-4.69-0 however Kern County did not approve the construction permits due to planned road widening at the project site. The Project Team reevaluated the planned isolation point and identified two alternate isolation points. The Project Team determined that the installation of two new valves, one north of MLV 7039-4.69-0, and one west of MLV 7039-4.69-0 would enable rapid isolation, thereby achieving Valve

¹ See Workpapers supporting Amended Pipeline Safety Enhancement Plan (PSEP) of SoCalGas and SDG&E, submitted on December 2, 2011, at WP-IX-2-14 through WP-IX-2-25 (A.11-11-002 Exh. SCG-32).

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

Enhancement Plan objectives. The Project Team revised the scope to the installation and automation of two new valves at these locations.

4. Final Project Scope: The final project scope consists of the automation of two new MLVs that included the removal of one MLV, the installation of two MLVs, the installation of two new actuators, the installation of two new vaults to house the actuators, the installation of new power equipment, the installation of new communications equipment, the installation of the necessary automation equipment at the sites, and the removal of MLV 7039-4.69-0.

Table 2: Final Project Scope

| Final Project Scope | | | | | |
|---------------------|------|---------|------------------------------|-------------------|----------|
| Line | Mile | Valve # | Valve Size (confidential) | Installation Type | Function |
| 38-7030 | - | 1 | | NV/VT | RCV |
| 7039 | 5.14 | 0 | | NV/VT | ASV/RCV |

B. Site Evaluation and Planning

SoCalGas initiated the planning process for the Taft Valve Enhancement Project - Hageman and Renfro by performing a pre-design site walk to determine the existing conditions and assess any potential impact on the design. Key factors that influenced the engineering and design of this project are as follows:

MLV 38-7030-1

1. Site Description: The site is located in a residential area west of the intersection of Hageman Road and Renfro Road in Bakersfield.
2. Land Issues: During the pre-design of this project, the Project Team noted that excavations will impact the street as well as the adjacent sidewalk.
3. DOT Class: This project site is in a Class 3 location.
4. Power Source: There was no preexisting power source. The Project Team installed new power equipment at the site.

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

5. Communication Technology: There was no preexisting communications equipment. The Project Team installed new communications equipment at this site.

MLV 7039-5.14-0

1. Site Description: The project is next to a residential development and an agricultural field on the heavily traveled Renfro Road. This site location is approximately half a mile north of the initial site location.
2. Land Issues: During the pre-design of this project, the Project Team noted that excavations will impact the street as well as the adjacent sidewalk.
3. DOT Class: This project site is in a Class 3 location.
4. Power Source: There was no existing power source. The Project Team installed new power equipment at the site.
5. Communication Technology: There was no preexisting communications equipment. The Project Team installed new communications equipment at the site.

C. Engineering, Design, and Planning Factors

SoCalGas reviewed drawings and records, contacted internal planning groups, communicated with external stakeholders, conducted survey activity, performed potholing of the area to identify the presence of underground utilities and substructures, and completed a site walk. Key factors that influenced the engineering and design of the Project are as follows:

MLV 38-7030-1

1. Engineering Assessment: During the site evaluation, the Project Team verified that the automation of the new valves would achieve the objectives Valve Enhancement Plan objectives.
2. Valve Details: There was no existing valve. The Project Team installed a new Class 600 ball valve.
3. Actuator Details: There was no existing actuator. The Project Team installed a new actuator.

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

4. Customer Impact: The installation of the new MLV required a shut in of Supply Line 38-7030. The Project Team utilized stopple fittings to avoid any service disruptions to customers.
5. Community Impact: The Project Team restricted public access to the sidewalk during construction.
6. Substructures: The Project Team did not identify any existing substructures that affected the design and engineering at this site.
7. Environmental: The Project Team did not identify any notable environmental concerns at the site. An environmental monitor performed routine site visits during construction.
8. Permit Restrictions: The Project Team obtained excavation and traffic control permits from Kern County.
9. Land Use: The Project Team obtained a non-exclusive easement for the installation of vaults and panels in public roadways. The Project Team obtained a Temporary Right of Entry (TRE) for the laydown yard that was shared between the two project sites.
10. Traffic Control: The Project Team closed one lane of Hageman Road during construction for excavation. Flagmen, k-rails, and signage were utilized for traffic control.

MLV 7039-5.14-0


1. Engineering Assessment: During the site evaluation, the Project Team verified that the automation of the new valves would achieve the objectives Valve Enhancement Plan objectives..
2. Valve Details:
 - a. MLV 7039-4.69-0: The preexisting valve was removed.
 - b. MLV 7039-5.14-0: There was no existing valve. The Project Team installed a new Class 600 ball valve.
3. Actuator Details: There was no existing actuator. The Project Team installed a new actuator.

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

4. Customer Impact: The Project Team determined that the existing line could be shut in without an impact to customers.
5. Community Impact: The Project Team restricted public access to the sidewalk during construction.
6. Substructures: The Project Team did not identify any existing substructures that affected the design and engineering at this site.
7. Environmental: The Project Team did not identify any notable environmental concerns at the site. An environmental monitor performed routine site visits during construction.
8. Permit Restrictions: The Project Team obtained excavation and traffic control permits from Kern County.
9. Land Use: The Project Team obtained a TRE for the laydown yard that was shared between both project sites.
10. Traffic Control: The Project Team closed one lane of Renfro Road during construction for excavation. Flagmen, k-rails, and signage were utilized for traffic control.

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

Figure 4: Taft Valve Enhancement Project Hageman and Renfro - Project Schematic

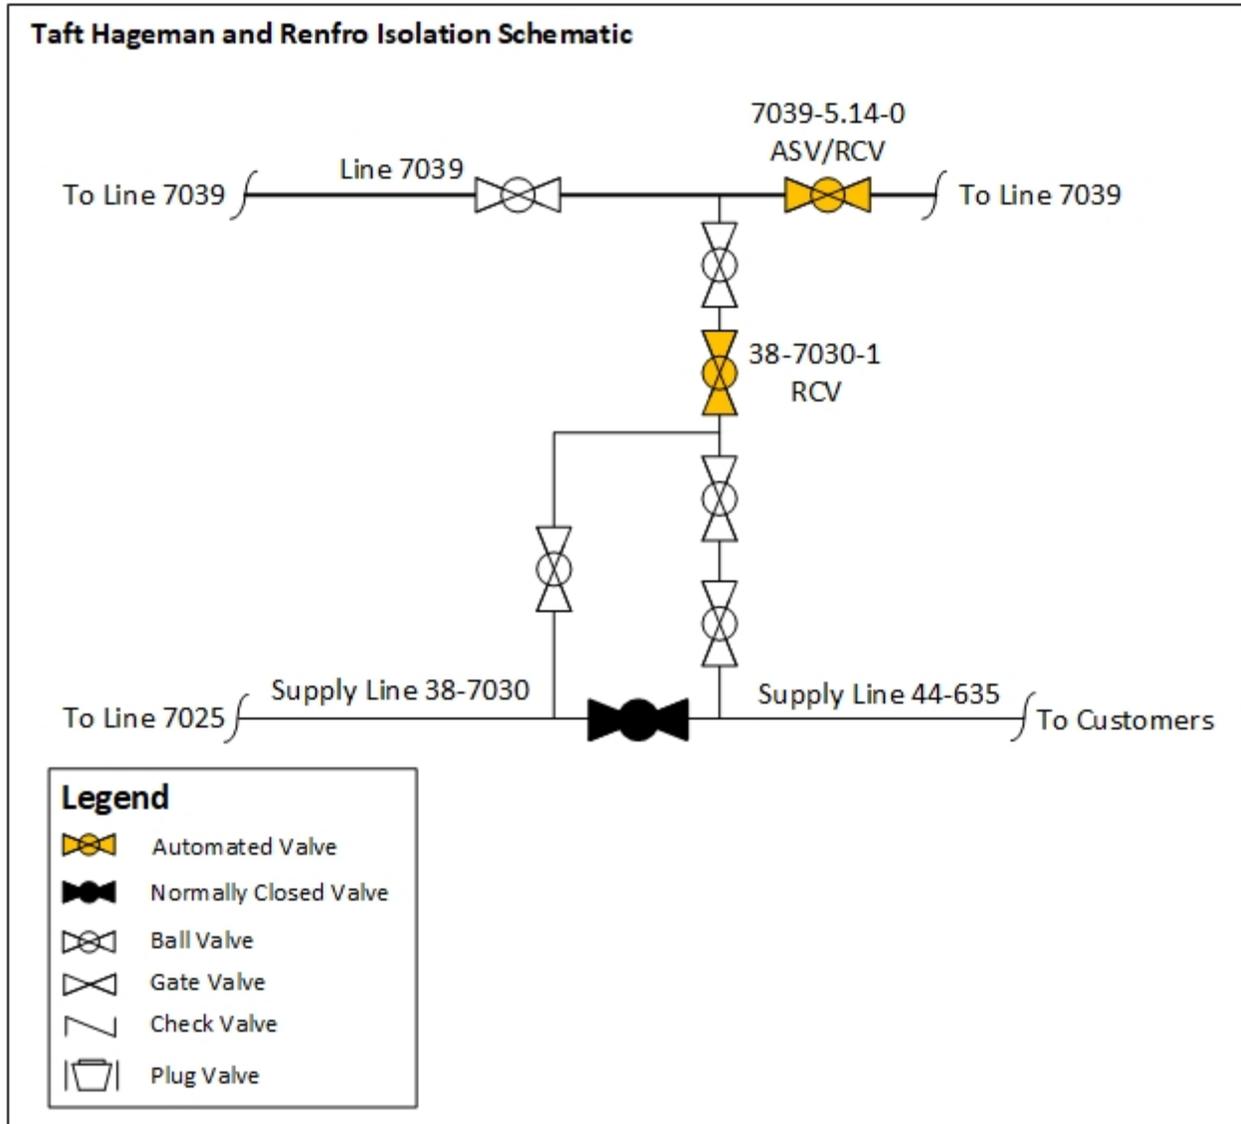

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

D. Scope Changes

SoCalGas did not make any notable scope changes during detailed design.

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

III. CONSTRUCTION

A. Construction Contractor Selection

The Project Team prepared an initial cost estimate based on the preliminary design. Following completion of the engineering, design, and planning activities described above, the Project Team directed the Performance Partner (Mechanical Construction Contractor) and Alliance Partner (Electrical Contractor) to prepare cost estimates based on a more detailed engineering design package, which included the updated design described in the discussion of notable changes in scope above.

1. SoCalGas' Preliminary Mechanical Construction Contractor Estimate (confidential): SoCalGas' preliminary cost estimate for construction was [REDACTED].
2. Mechanical Construction Contractor's Target Price Estimate (confidential): The Mechanical Construction Contractor's cost estimate was [REDACTED], which was [REDACTED] than SoCalGas' preliminary cost estimate for construction.
3. SoCalGas' Preliminary Electrical Contractor Estimate (confidential): SoCalGas' preliminary cost estimate for construction was [REDACTED].
4. Electrical Contractor's Estimate (confidential): The Electrical Contractor's estimate was [REDACTED], which was [REDACTED] than SoCalGas' preliminary cost estimate.

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

B. Construction Schedule

Table 3: Construction Timeline

| | |
|------------------------------|------------|
| Construction Start Date | 11/09/2018 |
| Construction Completion Date | 04/25/2019 |
| Days on Site | 88 days |
| Commissioning Date | 10/17/2019 |

The Project Team completed all construction activities as soon as practicable prior to commissioning. Finalization of commissioning activities is dependent on electrical utility connections, and system and/or resource availability.

C. Changes During Construction

The conditions summarized below were encountered during construction. Activities to address or mitigate these conditions resulted in approximately \$452,000 in change orders.

MLV 38-7030-1

1. Constructability Issues: During potholing, the construction contractor discovered that the proposed location for a new stopple installation did not satisfy the depth requirements of the stopple fitting. The Project Team relocated the stopple location approximately 1,000 feet west of the original location.
2. Utility Coordination: The original planned location for the electrical installation from was relocated to the opposite side of Hageman Road. The Project Team utilized a horizontal directional drill to cross Hageman Road while installing the new conduit.
3. Tie-In: SoCalGas requested additional personnel to support with equipment installation, and fire watch during the tie-in due to complicated gas handling procedures.

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

4. Traffic: The placement of the K-rails, as part of the traffic control plans, did not allow for a 14 foot wide lane. The City of Bakersfield requested that the Project Team repaint the double yellow centerline on Hageman Road to achieve the required width.
5. Constructability Issues: Construction crews determined that two trees and some communication lines would interfere with the installation of the new vault. The Construction Contractor removed the two trees and rerouted the communication lines to facilitate the installation of the new vault.

MLV 7039-5.14-0

1. Tie-in: The tie-in was delayed due to a work restriction by SoCalGas on Line 7039 resulting in standby charges. The tie-in also extended beyond the 24 hours included in the TPE.
2. Schedule: The construction duration extended 28 days beyond what was planned. This resulted in additional charges for shoring, equipment, security, and other overheads during construction.
3. Weather: Heavy rain and poor soil conditions resulted in a cave-in of the excavation during construction. The Construction Contractor removed the existing soil and backfilled with 1-sack slurry to prevent any future cave-ins. Construction was also delayed multiple times due to fog and rain.

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

Figure 5: MLV and Framework Prior to Fabrication of the Cast-in-Place Vault



Final Report for Taft Valve Enhancement Project - Hageman and Renfro

D. Commissioning and Site Restoration

Commissioning activities included site restoration, final inspections, and placement of the valves into service. During this stage, SoCalGas successfully performed site acceptance testing and conducted point-to-point verification with SoCalGas Gas Control personnel for the newly-automated valves, and transferred ownership of the new equipment to Field Operations. Closeout activities included development of final drawings, the reconciliation package, and updates to company recordkeeping systems to reflect the completed scope of work. The site was commissioned on October 17, 2019, as summarized in Table 3.

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

IV. PROJECT COSTS

A. Cost Avoidance Actions

SoCalGas exercised due diligence in the design, planning, and construction activities for this project to minimize or avoid costs when prudent to do so. As discussed above, the Project Team reviewed existing records, communicated with external stakeholders, and conducted a site walk to incorporate the site conditions in the project plan and design. The Project Team utilized a single laydown yard for both project sites in the installation of the two MLVs.

B. Cost Estimates

Based on the preliminary design, once the preliminary project scope was confirmed and engineering, design, and planning activities were underway, SoCalGas prepared an estimate of the Direct Costs of the Project in the amount of \$5,936,207. The Project Team considered the conditions known at the time to prepare the preliminary Direct Cost estimate. This estimate reflects the projected Labor, Material, and Services costs anticipated to be incurred to execute the Project, based on initial design plans.

SoCalGas estimated Indirect Costs of the Project based on the estimated Direct Costs and other project-related variables.

C. Actual Direct and Indirect Costs

Actual Direct Costs reflect the Labor, Material, and Services costs incurred to execute the Project. Actual Indirect Costs reflect costs for incremental overhead loaders in accordance with Company overhead allocation policies. The total loaded cost of the Project is \$8,150,072.

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

Table 4: Estimated and Actual Direct Costs and Variances²

| Direct Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|------------------------------------|------------------|------------------|--------------------|
| Company Labor | 525,343 | 351,586 | (173,757) |
| Materials | 565,414 | 499,634 | (65,779) |
| Mechanical Construction Contractor | 2,589,877 | 3,582,744 | 992,867 |
| Electrical Contractor | 184,698 | 205,974 | 21,276 |
| Construction Management & Support | 426,755 | 394,050 | (32,704) |
| Environmental | 131,401 | 146,667 | 15,266 |
| Engineering & Design | 429,024 | 975,973 | 546,949 |
| Project Management & Services | 208,681 | 62,308 | (146,373) |
| ROW & Permits | 250,118 | 82,475 | (167,643) |
| GMA | 624,897 | 771,547 | 146,650 |
| Total Direct Costs | 5,936,207 | 7,072,959 | 1,136,752 |

Table 5: Estimated and Actual Indirect Costs, Total Costs, and Variances³

| Indirect Costs/Total Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|---------------------------------|------------------|------------------|--------------------|
| Overheads | 890,422 | 775,933 | (114,489) |
| AFUDC | 1,304,102 | 259,763 | (1,044,339) |
| Property Taxes | 327,446 | 41,417 | (286,029) |
| Total Indirect Costs | 2,521,970 | 1,077,113 | (1,444,857) |
| Total Direct Costs | 5,936,207 | 7,072,959 | 1,136,752 |
| Total Loaded Costs | 8,458,177 | 8,150,072 | (308,105) |

² Values may not add to total due to rounding.

³ Ibid.

Final Report for Taft Valve Enhancement Project - Hageman and Renfro

V. CONCLUSION

SoCalGas enhanced the safety of their integrated natural gas system by prudently executing the Taft Valve Enhancement Project – Hageman and Renfro. Through this Valve Enhancement Project, SoCalGas successfully installed and automated two new mainline valves to achieve the objective of enabling rapid system isolation to portions of Line 7039 and Supply Line 38-7030 in the City of Bakersfield. The total loaded cost of the Project is \$8,150,072.

SoCalGas executed this project prudently through designing and executing the Project to support the Valve Enhancement Plan isolation objectives; coordinating and bundling two valves sites into one comprehensive package to capture efficiencies through coordinated scheduling of construction crews; installing two new mainline valves, two new actuators, and installing equipment necessary to bring power and communication capabilities to these valves to enable rapid system isolation of portions of Line 7039 and Supply Line 38-7030 located in the City of Bakersfield.

SoCalGas engaged in prudent cost avoidance efforts to complete this safety enhancement at a reasonable cost by carefully planning and coordinating construction activity, and by limiting the number of mobilizations and laydown yards across two different project sites to maximize efficiencies and reduce customer and community impacts.

End of Taft Valve Enhancement Project - Hageman and Renfro Final Report

Final Report for Taft Valve Enhancement Project – Sycamore Road

I. TAFT VALVE ENHANCEMENT PROJECT – SYCAMORE ROAD

A. Background and Summary

The Taft Valve Enhancement Project – Sycamore Road consists of valve enhancements made to an existing mainline valve (MLV) located in the Kern River Oil Field within Kern County. Through this project, SoCalGas enhanced the safety of their integrated gas transmission system by enabling the rapid detection of a significant change in pipeline pressure and remote isolation and depressurization of Line 7039 in the event of a pipeline rupture. SoCalGas installed a new actuator, new fencing, new power equipment, new communications equipment, and the necessary automation equipment at the site. The total loaded project cost is \$1,340,306.

The Taft Valve Enhancement Project – Sycamore Road construction site is within an existing SoCalGas facility in the Kern River Oil Field near Bakersfield. There are no buildings or vegetation in the area. SoCalGas bundled this valve project with three additional valve projects, the Taft Valve Enhancement Projects – 7th Standard, Buttonwillow, and Hageman and Renfro, into a single valve bundle to gain efficiencies in engineering, planning, and construction activities. The Project Team tracked the projects separately to more effectively track cost and streamline project closeout for individual sites. This workpaper describes the construction activities and costs of the Taft Valve Enhancement Project – Sycamore Road.

Final Report for Taft Valve Enhancement Project – Sycamore Road

Table 1: General Project Information

| Taft Valve Enhancement Project – Sycamore Road | | | |
|---|---------------------|----------------|--------------|
| Location | City of Bakersfield | | |
| Days on Site | 31 days | | |
| Construction Start | 08/21/2017 | | |
| Construction Finish | 11/29/2017 | | |
| Commissioning Date | 08/22/2018 | | |
| Valve Upgrades | | | |
| Valve Number | 7039-16.99-0 | | |
| Valve Type | Existing – Ball | | |
| Actuator | New | | |
| Actuator Above-/Below-Grade | Above-Grade | | |
| ASV | Yes | | |
| RCV | Yes | | |
| Site Upgrades | | | |
| Vault | None | | |
| Power | New – Solar | | |
| Communication | New – Radio | | |
| SCADA Panel | New | | |
| Equipment Shelter | None | | |
| Fencing | New | | |
| Project Costs (\$) | Capital | O&M | Total |
| Loaded Project Costs | 1,340,306 | 0 | 1,340,306 |
| Disallowed Costs | | | |

Final Report for Taft Valve Enhancement Project – Sycamore Road

B. Maps and Images

Figure 1: Taft Valve Enhancement Sycamore Road



Final Report for Taft Valve Enhancement Project – Sycamore Road

Figure 2: Satellite Image of Taft Valve Enhancement Project – Sycamore Road



Final Report for Taft Valve Enhancement Project – Sycamore Road

II. ENGINEERING, DESIGN, AND PLANNING

A. Project Scope

SoCalGas presented a conceptual project scope in workpapers supporting the Valve Enhancement Plan in the 2011 PSEP filing.¹ This conceptual scope did not include this project. SoCalGas reviewed available information, performed a detailed system flow analysis, and identified this valve as a candidate for enhancement to provide the planned isolation. The final project scope is summarized in Table 2 below.

1. 2011 PSEP Filing: SoCalGas did not identify this valve for automation to achieve the objective of rapid system isolation.
2. Updated Scope: SoCalGas determined that the automation of MLV 7039-16.99-0 would enable rapid isolation, thereby achieving Valve Enhancement Plan objectives.
3. Engineering, Design, and Constructability: The Project Team did not make any notable changes in scope to the engineering and design of this project.
4. Final Project Scope: The final project scope consists of the automation of one MLV, the installation of a new actuator, the installation of power equipment, the installation of communications equipment, the installation of new fencing, and the installation of the necessary automation equipment at the site.

Table 2: Final Project Scope

| Final Project Scope | | | | | |
|---------------------|-------|---------|---------------------------------------|-------------------|----------|
| Line | Mile | Valve # | Valve Size (<i>confidential</i>) | Installation Type | Function |
| 7039 | 16.99 | 0 | | A/AG | ASV/RCV |

¹ See Workpapers supporting Amended Pipeline Safety Enhancement Plan (PSEP) of SoCalGas and SDG&E, submitted on December 2, 2011, at WP-IX-2-14 through WP-IX-2-25 (A.11-11-002 Exh. SCG-32).

Final Report for Taft Valve Enhancement Project – Sycamore Road

B. Site Evaluation and Planning

SoCalGas and initiated the planning process for the Taft Valve Enhancement Project – Sycamore Road by performing a pre-design site walk to determine the existing conditions and assess any potential impact on the design. Key factors that influenced the engineering and design of this project are as follows:

1. Site Description: This project site is an existing SoCalGas facility in the Kern River Oil Field outside of Bakersfield. There are no buildings or vegetation in the area.
2. Land Issues: During the pre-design site walk, the Project Team noted that the existing station would need to be expanded to accommodate the additional equipment.
3. DOT Class: This project site is in a Class 1 location. SoCalGas selected this MLV for automation to isolate a Class 3 location upstream of this valve, and to satisfy the objectives of the PSEP Valve Enhancement Plan.
4. Power Source: There was no preexisting power equipment at this site. The Project Team installed new power equipment.
5. Communication Technology: There was no preexisting communications equipment. The Project Team installed new communications equipment.

C. Engineering, Design, and Planning Factors

SoCalGas reviewed drawings and records, contacted internal planning groups, communicated with external stakeholders, conducted survey activity, and completed a site walk. Key factors that influenced the engineering and design of the Project are as follows:


1. Engineering Assessment: During the site evaluation, the Project Team confirmed the existing technology and verified that the station would need to be expanded to accommodate the new equipment.
2. Valve Details: The existing valve was a manually operated Class 600 ball valve, which was reused by the Project Team.

Final Report for Taft Valve Enhancement Project – Sycamore Road

3. Actuator Details: There was no existing actuator, so the Project Team installed a new actuator.
4. Customer Impact: The Project Team did not identify any anticipated service disruptions to customers.
5. Community Impact: The Project Team did not anticipate any notable impact to the community from this Project.
6. Substructures: The Project Team did not identify any existing substructures that affected the design and engineering at this site.
7. Environmental: The Project Team did not identify any notable environmental concerns at the site. An environmental monitor performed routine site visits during construction.
8. Permit Restrictions: There were no special permits or permit restrictions for this project.
9. Land Use: The Project Team obtained a new easement for the expansion of the existing SoCalGas facility. The Project Team also obtained a Temporary Right of Entry for construction. The Project Team utilized the area around the facility as a laydown yard.
10. Traffic Control: The Project Team did not identify any traffic control needs at the site.

Final Report for Taft Valve Enhancement Project – Sycamore Road

Figure 3: Taft Valve Enhancement Project Schematic – Sycamore Road

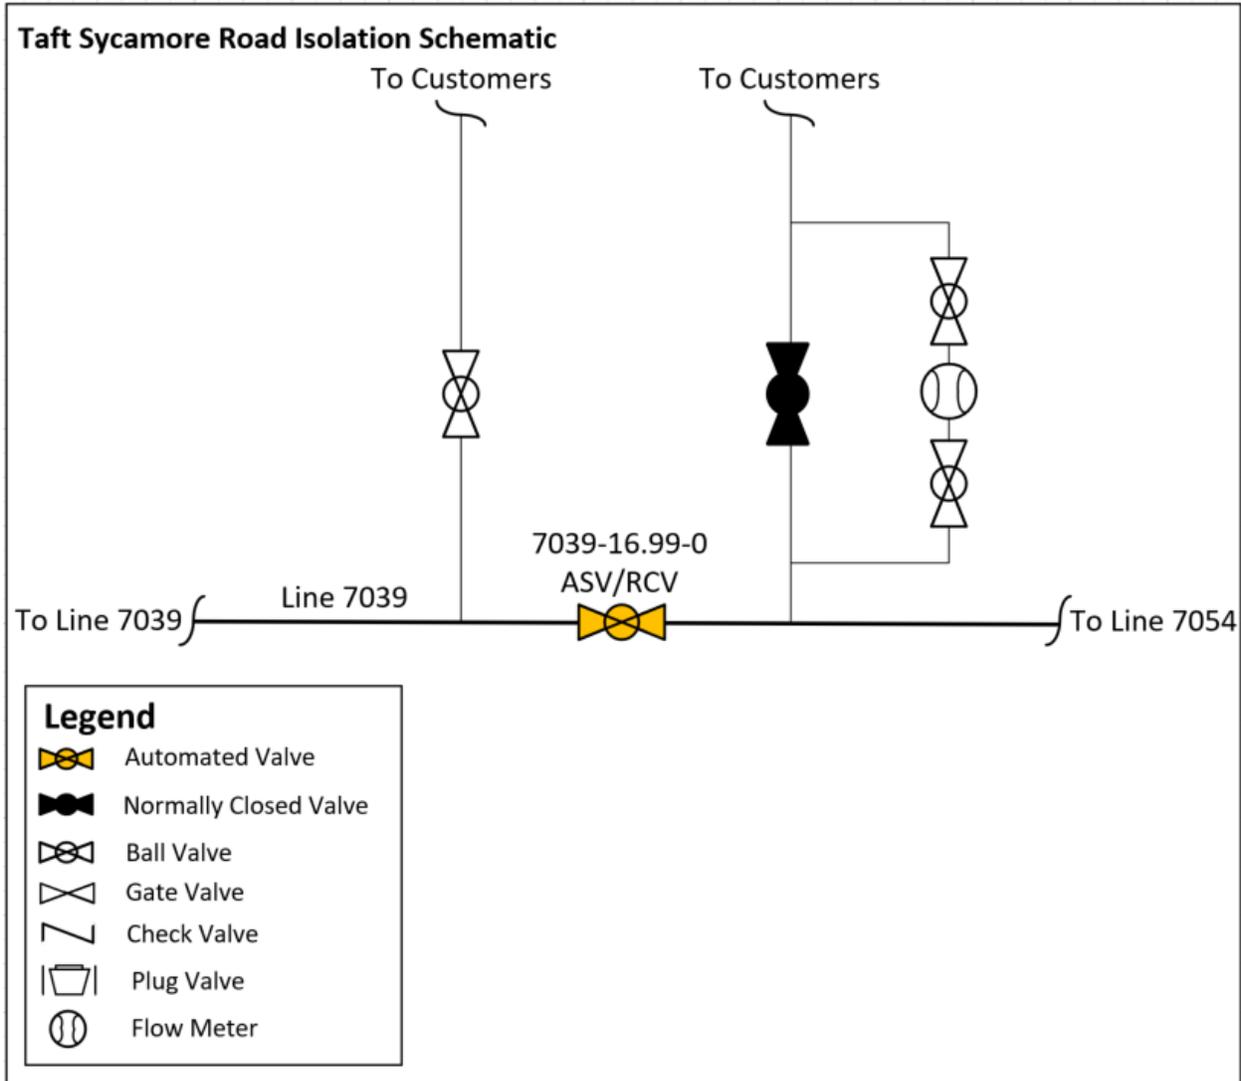

Final Report for Taft Valve Enhancement Project – Sycamore Road

D. Scope Changes

Through engineering, design, and planning activities, SoCalGas determined that changes in scope were appropriate to enhance the design of the Project and address engineering factors. As a result, the preliminary cost estimate does not fully reflect the final scope. A notable change in scope was made after the preliminary cost estimate was developed and approved. The Project Team initially planned to install a ground grid at the new station. After the creation of the Stage 3 Estimate, the Project Team determined that the ground grid was not necessary.

Final Report for Taft Valve Enhancement Project – Sycamore Road

III. CONSTRUCTION

A. Construction Contractor Selection

The Project Team prepared an initial cost estimate based on the preliminary design. Following completion of the engineering, design, and planning activities described above, the Project Team directed the Performance Partner (Mechanical Construction Contractor) and Alliance Partner (Electrical Contractor) to prepare cost estimates based on a more detailed engineering design package, which included the updated design described in the discussion of notable changes in scope above.

1. SoCalGas' Preliminary Mechanical Construction Contractor Estimate (confidential): SoCalGas' preliminary cost estimate for construction was [REDACTED].
2. Mechanical Construction Contractor's Target Price Estimate (confidential): The Mechanical Construction Contractor's cost estimate was [REDACTED], which was [REDACTED] than SoCalGas' preliminary cost estimate for construction.
3. SoCalGas' Preliminary Electrical Contractor Estimate (confidential): SoCalGas' preliminary cost estimate for construction was [REDACTED].
4. Electrical Contractor's Estimate (confidential): The Electrical Contractor's estimate was [REDACTED], which was [REDACTED] than SoCalGas' preliminary cost estimate.

Final Report for Taft Valve Enhancement Project – Sycamore Road

B. Construction Schedule

Table 3: Construction Timeline

| | |
|------------------------------|------------|
| Construction Start Date | 08/21/2017 |
| Construction Completion Date | 11/29/2017 |
| Days on Site | 31 days |
| Commissioning Date | 08/22/2018 |

The Project Team completed all construction activities as soon as practicable prior to commissioning. Finalization of commissioning activities is dependent on electrical utility connections, and system and/or resource availability.

C. Changes During Construction

SoCalGas successfully mitigated field conditions during construction in a manner that minimized potential impacts on project scope, cost, and schedule. As a result, these conditions did not result in any notable change orders.

Final Report for Taft Valve Enhancement Project – Sycamore Road

Figure 4: Excavation for new Actuator Installation in Foreground, Existing Pig Launcher in the Background



Final Report for Taft Valve Enhancement Project – Sycamore Road

D. Commissioning and Site Restoration

Commissioning activities included site restoration, final inspections, and placement of the valve into service. During this stage, SoCalGas successfully performed site acceptance testing and conducted point-to-point verification with Gas Control personnel for the newly-automated valve and transferred ownership of the new equipment to Field Operations. Closeout activities included development of final drawings, the reconciliation package, and updates to company recordkeeping systems to reflect the completed scope of work. During the development of the reconciliation package, SoCalGas determined that this valve will be known as MLV 7039-17.00-0. The site was commissioned on August 22, 2018, as summarized in Table 3.

Final Report for Taft Valve Enhancement Project – Sycamore Road

IV. PROJECT COSTS

A. Cost Avoidance Actions

SoCalGas exercised due diligence in the design, planning, and construction activities for this project to minimize or avoid costs when prudent to do so. As discussed above, the Project Team reviewed existing records, communicated with external stakeholders, and conducted a site walk to incorporate the known site conditions in the project plan and design. The Project Team bundled this project with the Taft Valve Enhancement Projects – 7th Standard, Buttonwillow, and Hageman and Renfro, coordinating engineering and construction activities between the project sites to minimize costs for the benefit of the customers.

B. Cost Estimates

Based on the preliminary design, once the preliminary project scope was confirmed and engineering, design, and planning activities were underway, SoCalGas prepared an estimate of the Direct Costs of the Project in the amount of \$1,661,767. The Project Team considered the conditions known at the time to prepare the preliminary Direct Cost estimate. This estimate reflects the projected Labor, Material, and Services costs anticipated to be incurred to execute the Project, based on initial design plans.

SoCalGas estimated Indirect Costs of the Project based on the estimated Direct Costs and other project-related variables.

C. Actual Direct and Indirect Costs

Actual Direct Costs reflect the Labor, Material, and Services costs incurred to execute the Project. Actual Indirect Costs reflect costs for incremental overhead loaders in accordance with Company overhead allocation policies. The total loaded cost of the Project is \$ 1,340,306 .

Final Report for Taft Valve Enhancement Project – Sycamore Road

Table 4: Estimated and Actual Direct Costs and Variances²

| Direct Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|------------------------------------|------------------|------------------|--------------------|
| Company Labor | 189,750 | 74,529 | (115,221) |
| Materials | 146,803 | 86,195 | (60,608) |
| Mechanical Construction Contractor | 471,905 | 283,802 | (188,103) |
| Electrical Contractor | 187,905 | 98,231 | (89,674) |
| Construction Management & Support | 72,270 | 80,012 | 7,742 |
| Environmental | 118,085 | 78,305 | (39,780) |
| Engineering & Design | 179,676 | 274,310 | 94,634 |
| Project Management & Services | 132,753 | 27,479 | (105,274) |
| ROW & Permits | 11,550 | 19,739 | 8,189 |
| GMA | 151,070 | 126,874 | (24,196) |
| Total Direct Costs | 1,661,767 | 1,149,476 | (512,291) |

Table 5: Estimated and Actual Indirect Costs, Total Costs, and Variances³

| Indirect Costs/Total Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|---------------------------------|------------------|------------------|--------------------|
| Overheads | 226,350 | 118,454 | (107,896) |
| AFUDC | 118,884 | 62,809 | (56,075) |
| Property Taxes | 28,360 | 9,567 | (18,793) |
| Total Indirect Costs | 373,594 | 190,830 | (182,764) |
| Total Direct Costs | 1,661,767 | 1,149,476 | (512,291) |
| Total Loaded Costs | 2,035,362 | 1,340,306 | (695,055) |

² Values may not add to total due to rounding.

³ Ibid.

Final Report for Taft Valve Enhancement Project – Sycamore Road

V. CONCLUSION

SoCalGas enhanced the safety of its natural gas system by prudently executing the Taft Valve Enhancement Project – Sycamore Road. Through this Valve Enhancement Project, SoCalGas successfully automated one mainline valve to achieve the objective of enabling rapid system of a portion of Line 7039 located within Kern County. The total loaded cost of the Project is \$1,340,306.

SoCalGas executed this project prudently through designing and executing the project to support achievement of Valve Enhancement Plan isolation objectives, bundling four geographically proximate projects together to capture efficiencies through coordinated engineering and construction planning, and installing equipment necessary to bring power and communication capabilities to the site to enable rapid system isolation to a portion of Line 7039 located in Kern County.

SoCalGas engaged in prudent cost avoidance efforts to complete this safety enhancement at a reasonable cost by carefully planning and coordinating engineering and construction activities to maximize efficiencies and reduce customer and community impacts.

End of Taft Valve Enhancement Project – Sycamore Road Final Report

Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

I. VICTORVILLE COMMS VALVE ENHANCEMENT PROJECT – MLV 11

A. Background and Summary

The Victorville COMMS Valve Enhancement Project – MLV 11 consists of valve enhancements made to an existing mainline valve (MLV) located in an unincorporated area within San Bernardino County. Through this project, SoCalGas enhanced the safety of its natural gas transmission system by enabling the rapid detection of a significant change in pipeline pressure and remote isolation and depressurization of a portion of Line 3000 in the event of a pipeline rupture. SoCalGas installed new communications equipment and the necessary automation equipment at the site. The total loaded project cost is \$308,849.

The Victorville COMMS Valve Enhancement Project – MLV 11 construction site is within an existing SoCalGas facility in the desert environment near the unincorporated community of Ludlow. SoCalGas bundled this valve project with an additional valve project, Victorville COMMS Valve Enhancement Project – MLV 12 to gain efficiencies in engineering, planning, and construction activities. This workpaper describes the construction activities and costs of the Victorville COMMS Valve Enhancement Project – MLV 11. This Project's costs were shared by PSEP and the Operating District, with PSEP funding the activities that provided system isolation through automation of the mainline valve, and the Operating District funding separately the activities to install the new linebreak cabinet and canopy.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

Table 1: General Project Information

| Victorville COMMS Valve Enhancement Project – MLV 11 Valve Enhancement Project | | | |
|---|-----------------------|----------------|--------------|
| Location | San Bernardino County | | |
| Days on Site | 14 days | | |
| Construction Start | 10/22/2018 | | |
| Construction Finish | 01/10/2019 | | |
| Commissioning Date | 06/11/2019 | | |
| Valve Upgrades | | | |
| Valve Number | 3000-99.43-0 | | |
| Valve Type | Existing – Ball | | |
| Actuator | Existing | | |
| Actuator Above-/Below-Grade | Above Ground | | |
| ASV | Yes | | |
| RCV | No | | |
| Valve 11 Site Upgrades | | | |
| Vault | None | | |
| Power | Existing – Utility | | |
| Communication | New – Radio | | |
| SCADA Panel | None | | |
| Equipment Shelter | None | | |
| Fencing | Existing | | |
| Project Costs (\$) | Capital | O&M | Total |
| Loaded Project Costs | 308,849 | - | 308,849 |
| Disallowed Costs | - | - | - |

Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

B. Maps and Images

Figure 1: Satellite Image of Victorville COMMS Bundle Overview



Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

Figure 2: Satellite Image of Victorville COMMS Valve Enhancement Project – MLV 11



Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

II. ENGINEERING, DESIGN, AND PLANNING

A. Project Scope

SoCalGas and SDG&E presented a conceptual project scope in workpapers supporting the Valve Enhancement Plan in the 2011 PSEP filing.¹ This conceptual scope did not include this project. SoCalGas reviewed available information and performed a detailed system flow analysis that identified this valve as a candidate for enhancement to provide the planned isolation. The final project scope is summarized in Table 2 below.

1. 2011 PSEP Filing: SoCalGas and SDG&E did not identify this valve for automation to achieve the objective of rapid system isolation.
2. Updated Scope: SoCalGas determined that the automation of MLV 3000-99.93-0 would enable rapid isolation, thereby achieving Valve Enhancement Plan objectives.
3. Engineering, Design, and Constructability: The Project Team did not make any notable changes in scope to the engineering and design of this project.
4. Final Project Scope: The final project scope consists of the automation of one MLV, that included upgrades to the existing power equipment, the installation of communications equipment, and the installation of the necessary automation equipment at the site.

Table 2: Final Project Scope

| Final Project Scope | | | | | |
|---------------------|-------|---------|---------------------------------------|-------------------|----------|
| Line | Mile | Valve # | Valve Size (<i>confidential</i>) | Installation Type | Function |
| 3000 | 99.43 | 0 | ██████████ | COMM | ASV |

¹ See Workpapers supporting Amended Pipeline Safety Enhancement Plan (PSEP) of SoCalGas and SDG&E, submitted on December 2, 2011, at WP-IX-2-14 through WP-IX-2-25 (A.11-11-002 Exh. SCG-32).

Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

B. Site Evaluation and Planning

SoCalGas initiated the planning process for the Victorville COMMS Valve Enhancement Project – MLV 11 by performing a pre-design site walk to determine the existing conditions and assess any potential impact on the design. Key factors that influenced the engineering and design of this project are as follows:

1. Site Description: The project site is an existing SoCalGas facility in a desert environment near the unincorporated community of Ludlow approximately one mile North of Interstate 40. There is an existing chain link fence enclosing the site.
2. Land Issues: During the pre-design site walk, the Project Team noted that the existing facility can accommodate the new equipment. The Project Team noted that this project is located on lands owned by the Bureau of Land Management (BLM) within the Desert Renewable Energy Conservation Plan (DRECP) area.
3. DOT Class: This project site is in a class 1 location. SoCalGas selected this MLV for automation in accordance with the Valve Enhancement Plan as there was existing power and Lineguard technology, and to isolate known geological threats upstream and downstream of this valve.
4. Power Source: The site had existing utility power.
5. Communication Technology: There was no preexisting communications equipment. The Project Team installed new communications equipment at the site.

C. Engineering, Design, and Planning Factors

SoCalGas reviewed drawings and records, contacted internal planning groups, communicated with external stakeholders, and completed a site walk. Key factors that influenced the engineering and design of the Project are as follows:


1. Engineering Assessment: The Project Team did not make any notable changes in scope to the engineering and design of this project.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

2. Valve Details: The existing valve was a manually actuated Class 600 ball valve, which was reused by the Project Team.
3. Actuator Details: The existing actuator was a double-acting pneumatic actuator that the Project Team reused.
4. Customer Impact: The Project Team did not identify any anticipated service disruptions to customers.
5. Community Impact: The Project Team did not anticipate any notable impact to the community from this Project.
6. Substructures: The Project Team did not identify any existing substructures that affected the design and engineering at this site.
7. Environmental: The Project Team noted that this project is located on lands owned by the Bureau of Land Management (BLM) within the Desert Renewable Energy Conservation Plan (DRECP) area. A desert tortoise biological monitor was onsite full time during construction.
8. Permit Restrictions: There were no special permits or permit restrictions for this project site.
9. Land Use: The Project Team acquired a Temporary Right of Way (ROW) from the County of San Bernardino. The Project Team performed all work within the ROW.
10. Traffic Control: The Project Team did not identify any traffic control needs at the site.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

Figure 3: Victorville COMMS Valve Enhancement Project – MLV 11 Schematic

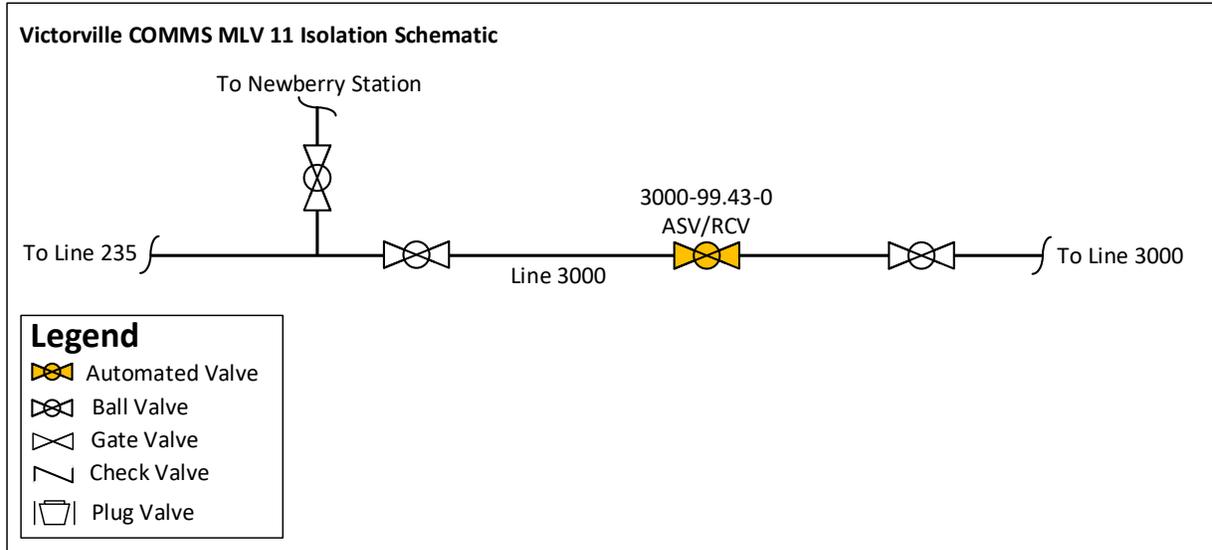

Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

D. Scope Changes

SoCalGas did not make any notable scope changes during detailed design.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

III. CONSTRUCTION

A. Construction Contractor Selection

The Project Team prepared an initial cost estimate based on the preliminary design. Following completion of the engineering, design, and planning activities described above, the Project Team directed the Alliance Partner (Electrical Contractor) to prepare cost estimates based on a more detailed engineering design package. As indicated above, there were no notable changes in scope between the time when the Project Team prepared the preliminary cost estimate and when the Alliance Partner prepared and submitted their estimates. The estimated values below include PSEP and non-PSEP work, whereas Tables 4 and 5 include estimated and actual values for PSEP work only.

1. SoCalGas' Preliminary Mechanical Construction Contractor Estimate (confidential): SoCalGas' preliminary cost estimate for construction was [REDACTED].
2. Mechanical Construction Contractor's Target Price Estimate (confidential): The Mechanical Construction Contractor's cost estimate was [REDACTED], which was [REDACTED] than SoCalGas' preliminary cost estimate for construction.
3. SoCalGas' Preliminary Electrical Contractor Estimate (confidential): SoCalGas' preliminary cost estimate for construction was [REDACTED].
4. Electrical Contractor's Estimate (confidential): The Electrical Contractor's estimate was [REDACTED], which was [REDACTED] than SoCalGas' preliminary cost estimate.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

B. Construction Schedule

Table 3: Construction Timeline

| | |
|------------------------------|------------|
| Construction Start Date | 10/22/2018 |
| Construction Completion Date | 01/10/2019 |
| Days on Site | 14 days |
| Commissioning Date | 06/11/2019 |

The Project Team completed all construction activities as soon as practicable prior to commissioning. Finalization of commissioning activities is dependent on electrical utility connections, and system and/or resource availability.

C. Changes During Construction

SoCalGas successfully mitigated field conditions during construction in a manner that minimized potential impacts on project scope, cost, and schedule. As a result, these conditions did not result in any notable change orders.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

Figure 4: Partial Backfill of Conduit Trench



Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

D. Commissioning and Site Restoration

Commissioning activities included site restoration, final inspections, and placement of the valve into service. During this stage, SoCalGas successfully performed site acceptance testing and conducted point-to-point verification with Gas Control personnel for the newly-automated valve, and transferred ownership of the new equipment to Field Operations. Closeout activities included development of final drawings, the reconciliation package, and updates to company recordkeeping systems to reflect the completed scope of work. The site was commissioned on June 11, 2019, as summarized in Table 3.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

IV. PROJECT COSTS

A. Cost Avoidance Actions

SoCalGas exercised due diligence in the design, planning, and construction activities for this project to minimize or avoid costs when prudent to do so. As discussed above, the Project Team reviewed existing records, communicated with external stakeholders, and conducted a site walk to incorporate the site conditions in the project plan and design. The Project Team bundled this valve project with an additional valve project, Victorville COMMS Valve Enhancement Project – Valve 12, into a single valve bundle to gain efficiencies in engineering, planning and construction activities to minimize costs for the benefit of customers.

B. Cost Estimates

Based on the preliminary design, once the preliminary project scope was confirmed and engineering, design, and planning activities were underway, SoCalGas prepared an estimate of the Direct Costs of the Project in the amount of \$291,150. The Project Team considered the conditions known at the time to prepare the preliminary Direct Cost estimate. This estimate reflects the projected Labor, Material, and Services costs anticipated to be incurred to execute the Project, based on initial design plans.

SoCalGas estimated Indirect Costs of the Project based on the estimated Direct Costs and other project-related variables.

C. Actual Direct and Indirect Costs

Actual Direct Costs reflect the Labor, Material, and Services costs incurred to execute the Project. Actual Indirect Costs reflect costs for incremental overhead loaders in accordance with Company overhead allocation policies. The total loaded cost of the Project is \$308,849.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

Table 4: Estimated and Actual Direct Costs and Variances²

| Direct Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|------------------------------------|----------------|----------------|--------------------|
| Company Labor | 96,106 | 21,636 | (74,470) |
| Materials | 5,157 | 1,368 | (3,789) |
| Mechanical Construction Contractor | 76,859 | 62,051 | (14,808) |
| Electrical Contractor | 20,581 | 19,044 | (1,537) |
| Construction Management & Support | 0 | 5,345 | 5,345 |
| Environmental | 15,216 | 12,500 | (2,716) |
| Engineering & Design | 7,360 | 37,502 | 30,142 |
| Project Management & Services | 25,431 | 4,045 | (21,386) |
| ROW & Permits | 4,035 | 7,204 | 3,169 |
| GMA | 40,405 | 17,840 | (22,565) |
| Total Direct Costs | 291,150 | 188,535 | (102,615) |

Table 5: Estimated and Actual Indirect Costs, Total Costs, and Variances³

| Indirect Costs/Total Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|---------------------------------|----------------|----------------|--------------------|
| Overheads | 159,050 | 102,831 | (56,219) |
| AFUDC | 50,409 | 10,523 | (39,886) |
| Property Taxes | 11,818 | 6,960 | (4,858) |
| Total Indirect Costs | 221,277 | 120,313 | (100,964) |
| Total Direct Costs | 291,150 | 188,535 | (102,615) |
| Total Loaded Costs | 512,427 | 308,849 | (203,578) |

² Values may not add to total due to rounding.

³ Ibid.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 11

V. CONCLUSION

SoCalGas enhanced the safety of its gas system by prudently executing the Victorville COMMS MLV 11 Valve Enhancement Project. Through this Valve Enhancement Project, SoCalGas successfully automated one mainline valve to achieve the objective of enabling rapid system isolation to a portion of Line 3000 located in an unincorporated area within San Bernardino County. The total loaded cost of the Project is \$308,849.

SoCalGas executed this project prudently through designing and executing the project to support achievement of Valve Enhancement Plan isolation objectives, bundling two geographically proximate projects together to capture efficiencies through coordinated engineering, and installing equipment necessary to bring communication capabilities to the site to enable rapid system isolation of a portion of Line 3000 located in San Bernardino County.

SoCalGas engaged in prudent cost avoidance efforts to complete this safety enhancement at a reasonable cost by carefully planning and coordinating engineering and construction activities to maximize efficiencies and reduce customer and community impacts.

End of Victorville COMMS Valve Enhancement Project – MLV 11 Final Report

Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

I. VICTORVILLE COMMS VALVE ENHANCEMENT PROJECT – MLV 12

A. Background and Summary

The Victorville COMMS Valve Enhancement Project – MLV 12 site consists of valve enhancements made to an existing mainline valve (MLV) in San Bernardino County. Through this project, SoCalGas enhanced the safety of its natural gas transmission system by enabling the rapid detection of a significant change in pipeline pressure and remote isolation and depressurization of a portion of Line 3000 in the event of a pipeline rupture. SoCalGas expanded an existing SoCalGas facility, installed new power equipment, new communications equipment, and the necessary automation equipment at the site. The total loaded project cost is \$528,982.

The Victorville COMMS Valve Enhancement Project – MLV 12 construction site is within an existing SoCalGas facility located in a desert area outside of Victorville next to Interstate 40. SoCalGas bundled this valve project with an additional valve project, Victorville COMMS Valve Enhancement Project – MLV 11 to gain efficiencies in engineering, planning, and construction activities. This workpaper describes the construction activities and costs of the Victorville COMMS Valve Enhancement Project – MLV 12. This Project's costs were shared by PSEP and the Operating District, with PSEP funding the activities that provided system isolation through automation of the mainline valve, and the Operating District funding separately the activities to install the new linebreak cabinet and canopy.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

Table 1: General Project Information

| Victorville COMMS Valve Enhancement Project – MLV 12 | | | |
|---|-----------------------|----------------|--------------|
| Location | San Bernardino County | | |
| Days on Site | 18 days | | |
| Construction Start | 11/06/2017 | | |
| Construction Finish | 12/19/2017 | | |
| Commissioning Date | 05/22/2018 | | |
| Valve Upgrades | | | |
| Valve Number | 3000-110.93-0 | | |
| Valve Type | Existing – Ball | | |
| Actuator | Existing | | |
| Actuator Above-/Below-Grade | Above-Grade | | |
| ASV | Yes | | |
| RCV | No | | |
| Site Upgrades | | | |
| Vault | None | | |
| Power | New – Solar | | |
| Communication | New – Radio | | |
| SCADA Panel | None | | |
| Equipment Shelter | None | | |
| Fencing | New | | |
| Project Costs (\$) | Capital | O&M | Total |
| Loaded Project Costs | 528,982 | - | 528,982 |
| Disallowed Costs | - | - | - |

Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

B. Maps and Images

Figure 1: Victorville COMMS Bundle Overview



Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

Figure 2: Satellite Image of Victorville COMMS Valve Enhancement Project – MLV 12



Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

II. ENGINEERING, DESIGN, AND PLANNING

A. Project Scope

SoCalGas presented a conceptual project scope in workpapers supporting the Valve Enhancement Plan in the 2011 PSEP filing.¹ This conceptual scope did not include this project. SoCalGas reviewed available information and performed a detailed system flow analysis that identified this valve as a candidate for enhancement to provide the planned isolation. The final project scope is summarized in Table 2 below.

1. 2011 PSEP Filing: SoCalGas did not identify this valve for automation to achieve the objective of rapid system isolation.
2. Updated Scope: SoCalGas determined that the automation of MLV 3000-110.93-0 would enable rapid isolation, thereby achieving Valve Enhancement Plan objectives.
3. Engineering, Design, and Constructability: The Project Team did not make any notable changes in scope to the engineering and design of this project.
4. Final Project Scope: The final project scope consists of the automation of one MLV, the expansion of an existing facility, the installation of power equipment, the installation of communications equipment, and the installation of the necessary automation equipment at the site.

Table 2: Final Project Scope

| Final Project Scope | | | | | |
|---------------------|--------|---------|---------------------------------------|-------------------|----------|
| Line | Mile | Valve # | Valve Size (<i>confidential</i>) | Installation Type | Function |
| 3000 | 110.93 | 0 | | COMM | ASV |

¹ See Workpapers supporting Amended Pipeline Safety Enhancement Plan (PSEP) of SoCalGas and SDG&E, submitted on December 2, 2011, at WP-IX-2-14 through WP-IX-2-25 (A.11-11-002 Exh. SCG-32).

Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

B. Site Evaluation and Planning

SoCalGas initiated the planning process for the Victorville COMMS Valve Enhancement Project – MLV 12 by performing a pre-design site walk to determine the existing conditions and assess any potential impact on the design. Key factors that influenced the engineering and design of this project are as follows:

1. Site Description: This site is an existing SoCalGas facility in a desert area in San Bernardino County, next to Interstate 40.
2. Land Issues: During the site evaluation, the Project Team noted that the existing station would need to be expanded to accommodate the additional equipment. The Project Team noted that this project is located on lands owned by the Bureau of Land Management (BLM) within the Desert Renewable Energy Conservation Plan (DRECP) area.
3. DOT Class: This project site is in a Class 1 location. SoCalGas selected this MLV for automation in accordance with the Valve Enhancement Plan as there was existing power and Lineguard technology, and to isolate known geological threats upstream and downstream of this valve.
4. Power Source: The site had preexisting solar power. The Project Team installed new solar power equipment to accommodate the increased loads from the new automation equipment.
5. Communication Technology: There was no preexisting communications equipment. The Project Team installed new communications equipment at the site.

C. Engineering, Design, and Planning Factors


SoCalGas reviewed drawings and records, contacted internal planning groups, communicated with external stakeholders, conducted survey activity, and completed a site walk. Key factors that influenced the engineering and design of the Project are as follows:

Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

1. Engineering Assessment: The Project Team did not make any notable changes in scope to the engineering and design of this project.
2. Valve Details: The existing valve was a manually actuated Class 600 ball valve, which was reused by the Project Team.
3. Actuator Details: The existing actuator was a double-acting pneumatic actuator that the Project Team reused.
4. Customer Impact: The Project Team did not identify any anticipated service disruptions to customers.
5. Community Impact: The Project Team did not anticipate any notable impact to the community from this Project.
6. Substructures: The Project Team did not identify any existing substructures that affected the design and engineering at this site.
7. Environmental: The Project Team noted that this project is located on lands owned by the Bureau of Land Management (BLM) within the Desert Renewable Energy Conservation Plan (DRECP) area. A desert tortoise biological monitor was onsite full time during construction.
8. Permit Restrictions: There were no special permits or permit restrictions for this project.
9. Land Use: The Project Team performed all work within the existing SoCalGas easement.
10. Traffic Control: The Project Team did not identify any traffic control needs at the site.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

Figure 3: Victorville COMMS Valve Enhancement Project – MLV 12 Schematic

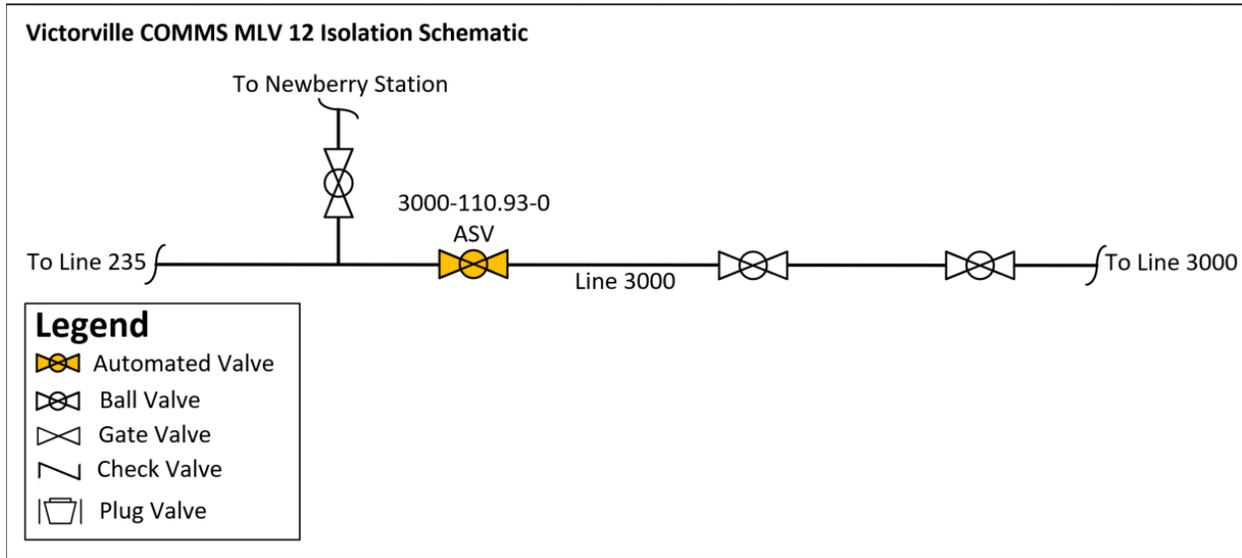

Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

D. Scope Changes

SoCalGas did not make any notable scope changes during detailed design.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

III. CONSTRUCTION

A. Construction Contractor Selection

The Project Team prepared an initial cost estimate based on the preliminary design. Following completion of the engineering, design, and planning activities described above, the Project Team directed the Performance Partner (Mechanical Construction Contractor) and Alliance Partner (Electrical Contractor) to prepare cost estimates based on a more detailed engineering design package. As indicated above, there were no notable changes in scope between the time when the Project Team prepared the preliminary cost estimate and when the Performance Partner and Alliance Partner prepared and submitted their estimates. The estimated values below include PSEP and non-PSEP work, whereas Tables 4 and 5 include estimated and actual values for PSEP work only.

1. SoCalGas' Preliminary Mechanical Construction Contractor Estimate (confidential): SoCalGas' preliminary cost estimate for construction was [REDACTED].
2. Mechanical Construction Contractor's Target Price Estimate (confidential): The Mechanical Construction Contractor's cost estimate was [REDACTED], which was [REDACTED] than SoCalGas' preliminary cost estimate for construction.
3. SoCalGas' Preliminary Electrical Contractor Estimate (confidential): SoCalGas' preliminary cost estimate for construction was [REDACTED].
4. Electrical Contractor's Estimate (confidential): The Electrical Contractor's estimate was [REDACTED], which was [REDACTED] than SoCalGas' preliminary cost estimate.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

B. Construction Schedule

Table 3: Construction Timeline

| | |
|------------------------------|------------|
| Construction Start Date | 11/06/2017 |
| Construction Completion Date | 12/19/2017 |
| Days on Site | 18 days |
| Commissioning Date | 05/22/2018 |

The Project Team completed all construction activities as soon as practicable prior to commissioning. Finalization of commissioning activities is dependent on electrical utility connections, and system and/or resource availability.

C. Changes During Construction

SoCalGas successfully mitigated field conditions during construction in a manner that minimized potential impacts on project scope, cost, and schedule. As a result, these conditions did not result in any notable change orders.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

Figure 4: Nitrogen Test for New Instrument Piping



Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

D. Commissioning and Site Restoration

Commissioning activities included site restoration, final inspections, and placement of the valve into service. During this stage, SoCalGas successfully performed site acceptance testing and conducted point-to-point verification with Gas Control personnel for the newly-automated valve, and transferred ownership of the new equipment to Field Operations. Closeout activities included development of final drawings, the reconciliation package, and updates to company recordkeeping systems to reflect the completed scope of work. The site was commissioned on May 22, 2018, as summarized in Table 3.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

IV. PROJECT COSTS

A. Cost Avoidance Actions

SoCalGas exercised due diligence in the design, planning, and construction activities for this project to minimize or avoid costs when prudent to do so. As discussed above, the Project Team reviewed existing records, communicated with external stakeholders, and conducted a site walk to incorporate known site conditions in the project plan and design. SoCalGas bundled this valve project with an additional valve project, Victorville COMMS Valve Enhancement Project – MLV 11 to gain efficiencies in engineering, planning, and construction activities.

B. Cost Estimates

Based on the preliminary design, once the preliminary project scope was confirmed and engineering, design, and planning activities were underway, SoCalGas prepared an estimate of the Direct Costs of the Project in the amount of \$323,473. The Project Team considered the conditions known at the time to prepare the preliminary Direct Cost estimate. This estimate reflects the projected Labor, Material, and Services costs anticipated to be incurred to execute the Project, based on initial design plans.

SoCalGas estimated Indirect Costs of the Project based on the estimated Direct Costs and other project-related variables.

C. Actual Direct and Indirect Costs

Actual Direct Costs reflect the Labor, Material, and Services costs incurred to execute the Project. Actual Indirect Costs reflect costs for incremental overhead loaders in accordance with Company overhead allocation policies. The total loaded cost of the Project is \$528,982.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

Table 4: Estimated and Actual Direct Costs and Variances^{2, 3}

| Direct Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|------------------------------------|----------------|----------------|--------------------|
| Company Labor | 105,151 | 66,470 | (38,681) |
| Materials | 5,157 | 6,411 | 1,254 |
| Mechanical Construction Contractor | 89,209 | 89,533 | 324 |
| Electrical Contractor | 20,581 | 54,218 | 33,637 |
| Construction Management & Support | - | 18,376 | 18,376 |
| Environmental | 20,488 | 49,093 | 28,605 |
| Engineering & Design | 7,360 | 72,481 | 65,121 |
| Project Management & Services | 25,565 | 9,981 | (15,584) |
| ROW & Permits | 4,035 | 5,281 | 1,246 |
| GMA | 45,927 | 57,448 | 11,521 |
| Total Direct Costs | 323,473 | 429,291 | 105,818 |

Table 5: Estimated and Actual Indirect Costs, Total Costs, and Variances⁴

| Indirect Costs/Total Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|---------------------------------|----------------|----------------|--------------------|
| Overheads | 176,562 | 86,374 | (90,188) |
| AFUDC | 59,845 | 10,570 | (49,275) |
| Property Taxes | 14,030 | 2,747 | (11,283) |
| Total Indirect Costs | 250,437 | 99,691 | (150,746) |
| Total Direct Costs | 323,473 | 429,291 | 105,818 |
| Total Loaded Costs | 573,910 | 528,982 | (44,928) |

² Values may not add to total due to rounding.

³ Values in table represent PSEP costs only.

⁴ Values may not add to total due to rounding.

Final Report for Victorville COMMS Valve Enhancement Project – MLV 12

V. CONCLUSION

SoCalGas enhanced the safety of its natural gas system by prudently executing the Victorville COMMS Valve Enhancement Project – MLV 12. Through this Valve Enhancement Project, SoCalGas successfully automated one MLV to achieve the objective of enabling rapid system isolation of a portion of Line 3000 in San Bernardino County. The total loaded cost of the Project is \$528,982.

SoCalGas executed this project prudently through designing and executing the project to support achievement of Valve Enhancement Plan isolation objectives, bundling two geographically proximate projects together, to capture efficiencies through coordinated engineering, and installing equipment necessary to bring power and communication capabilities to the site to enable rapid system isolation of a portion of Line 3000 located in San Bernardino County.

SoCalGas engaged in prudent cost avoidance efforts to complete this safety enhancement at a reasonable cost by carefully planning and coordinating engineering and construction activities to maximize efficiencies and reduce customer and community impacts.

End of Victorville COMMS Valve Enhancement Project – MLV 12 Final Report

Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost

I. WESTERN DEL REY VALVE ENHANCEMENT PROJECT – MISSISSIPPI AND ARMACOST

A. Background and Summary

This report describes the activities associated with the Western Del Rey Valve Enhancement Project – Mississippi and Armacost site, that consists of valve enhancements made to one existing mainline valve (MLV) located in the City of Los Angeles, in Los Angeles County. Through this project, SoCalGas enhanced the safety of their integrated gas transmission system by enabling the rapid detection of a significant change in pipeline pressure and remote isolation and depressurization of Lines 2003 and 407 in the event of a pipeline rupture. SoCalGas installed, new communications equipment, and the necessary automation equipment at the site. The total loaded project cost is \$494,984.

The Western Del Rey Valve Enhancement Project – Mississippi and Armacost site is an existing SoCalGas facility in an urban area on Mississippi Avenue in West Los Angeles. SoCalGas grouped this site with two additional sites, McLaughlin and Palms and Del Rey Junction, into a single valve bundle to gain efficiencies in engineering, and planning, activities. This workpaper speaks to the Mississippi and Armacost site.

Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost

Table 1: General Project Information

| Western Del Rey Mississippi and Armacost Valve Enhancement Project | | | |
|---|---------------------|----------------|--------------|
| Location | City of Los Angeles | | |
| Days on Site | 24 days | | |
| Construction Start | 12/06/2017 | | |
| Construction Finish | 04/15/2019 | | |
| Commissioning Date | 09/24/2018 | | |
| Valve Upgrades | | | |
| Valve Number | 2003-27.00-0 | | |
| Valve Type | Existing – Ball | | |
| Actuator | Existing | | |
| Actuator Above-/Below-Grade | Above-Grade | | |
| ASV | Yes | | |
| RCV | Yes | | |
| Site Upgrades | | | |
| Vault | None | | |
| Power | Existing – Utility | | |
| Communication | New – Radio | | |
| SCADA Panel | New | | |
| Equipment Shelter | Existing | | |
| Fencing | Existing | | |
| Project Costs (\$) | Capital | O&M | Total |
| Loaded Project Costs | 494,984 | - | 494,984 |
| Disallowed Costs | - | - | - |

Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost


B. Maps and Images

Figure 1: Western Del Rey Bundle Overview



Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost

Figure 2: Satellite Image of Western Del Rey Mississippi and Armacost Valve Enhancement Project

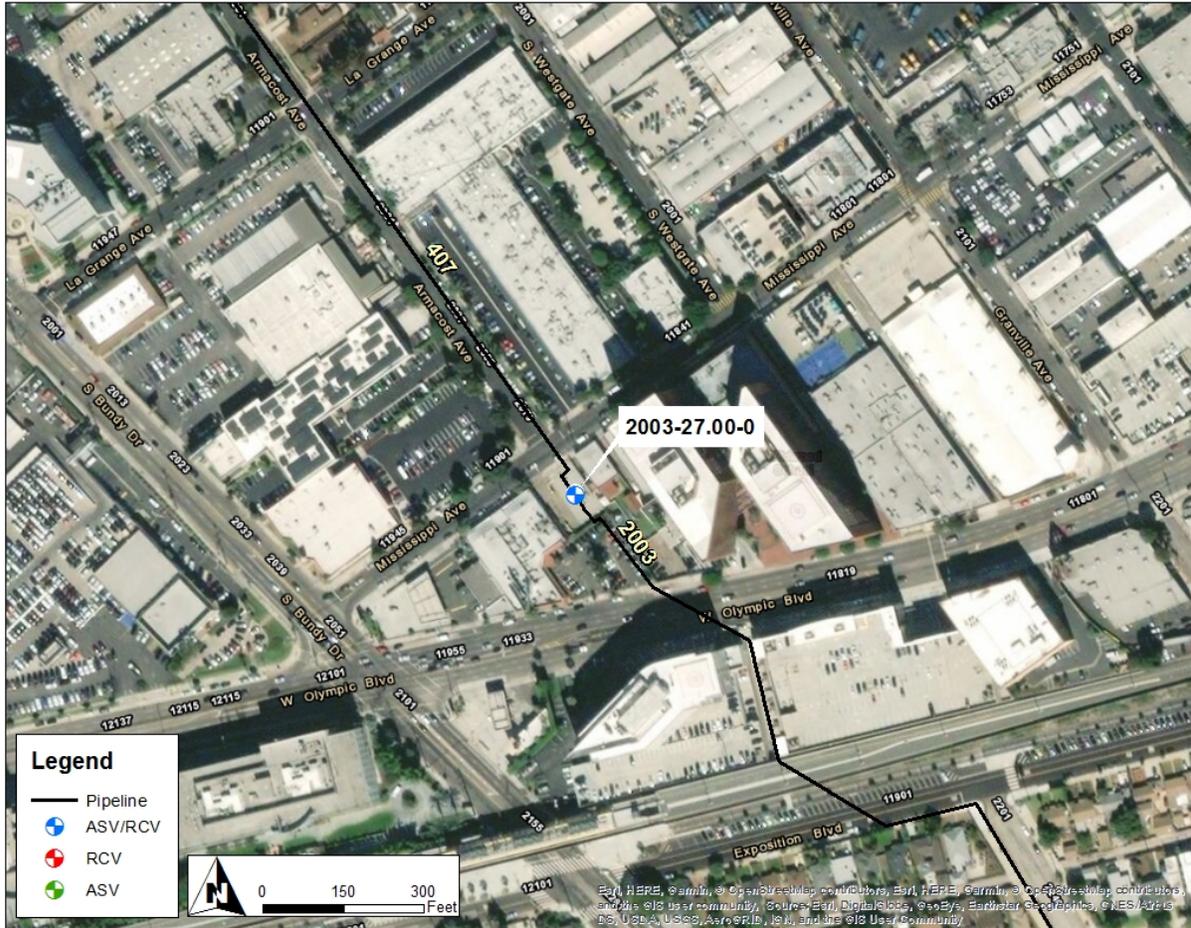

Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost

II. ENGINEERING, DESIGN, AND PLANNING

A. Project Scope

SoCalGas presented a conceptual project scope in workpapers supporting the Valve Enhancement Plan in the 2011 filing.¹ This conceptual scope identified MLV 2003-27.00-0 for automation to enable remote isolation to a portion of Lines 2003 and 407. Prior to initiating execution of the Project, SoCalGas reviewed available information and performed a detailed system flow analysis to validate the scope of the Project that confirmed that this enhancement will provide the planned isolation. The final project scope is summarized in Table 2 below.

1. 2011 PSEP Filing: SoCalGas identified MLV 2003-27.00-0 for automation to achieve the objective of rapid system isolation.
2. Updated Scope: Upon project initiation, SoCalGas reviewed the conceptual project scope and determined that this isolation point would achieve the transmission isolation objectives set forth in the Valve Enhancement Plan.
3. Engineering, Design, and Constructability: SoCalGas initially planned to replace the existing valve and actuator. The Project Team determined that the existing valve and actuator was compatible with the new PSEP linebreak technology. The Project Team updated the scope to reuse the existing valve and actuator.
4. Final Project Scope: The final project scope consists of the installation of new communications equipment, and the installation of the necessary automation equipment at the site.

¹ See Workpapers supporting Amended Pipeline Safety Enhancement Plan (PSEP) of SoCalGas and SDG&E, submitted on December 2, 2011, at WP-IX-2-14 through WP-IX-2-25 (A.11-11-002 Exh. SCG-32).

Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost

Table 2: Final Project Scope

| Final Project Scope | | | | | |
|---------------------|-------|---------|---------------------------------------|----------------------|----------|
| Line | Mile | Valve # | Valve Size (<i>confidential</i>) | Installation Type | Function |
| 2003 | 27.00 | 0 | | C/P | ASV/RCV |

B. Site Evaluation and Planning

SoCalGas initiated the planning process for the Western Del Rey Mississippi and Armacost Valve Enhancement Project by performing a pre-design site walk to determine the existing conditions and assess any potential impact on the design. Key factors that influenced the engineering and design of this project are as follows:

1. Site Description: This site is located in an existing SoCalGas facility in a high-density, commercial area in the City of Los Angeles on Mississippi Avenue.
2. Land Issues: During the pre-design site walk, the Project Team noted that the existing facility can accommodate the new equipment.
3. DOT Class: This project site is in a Class 4 location.
4. Power Source: The site has existing utility power.
5. Communication Technology: The existing communication equipment was incompatible with the PSEP standard design and was limited to alarm signals only, the Project Team installed new communications equipment at the site.

C. Engineering, Design, and Planning Factors


SoCalGas reviewed drawings and records, contacted internal planning groups, communicated with external stakeholders, conducted survey activity, and completed a site walk. Key factors that influenced the engineering and design of the Project are as follows:

Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost

1. Engineering Assessment: During the site evaluation, the Project Team confirmed the existing technology and verified that the station could accommodate the new equipment.
2. Valve Details: The existing valve was a manually actuated Class 300 ball valve that the Project Team reused.
3. Actuator Details: The existing actuator was a double-acting pneumatic actuator that the Project Team reused.
4. Customer Impact: The Project Team did not anticipate service disruptions to customers.
5. Community Impact: The Project Team did not anticipate any notable impacts to the community from this project.
6. Substructures: The Project Team did not identify any existing substructures that affected the design and engineering at this site.
7. Environmental: The Project Team did not identify any notable environmental concerns at the site. An environmental monitor performed routine site visits during construction.
8. Permit Restrictions: There were no special permits or permit restrictions for this project site.
9. Land Use: The Project Team used the existing SoCalGas facility as a laydown yard.
10. Traffic Control: The Project Team did not anticipate the use of traffic control at this site.

Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost

Figure 3: Western Del Rey Mississippi and Armacost Valve Enhancement Project Schematic

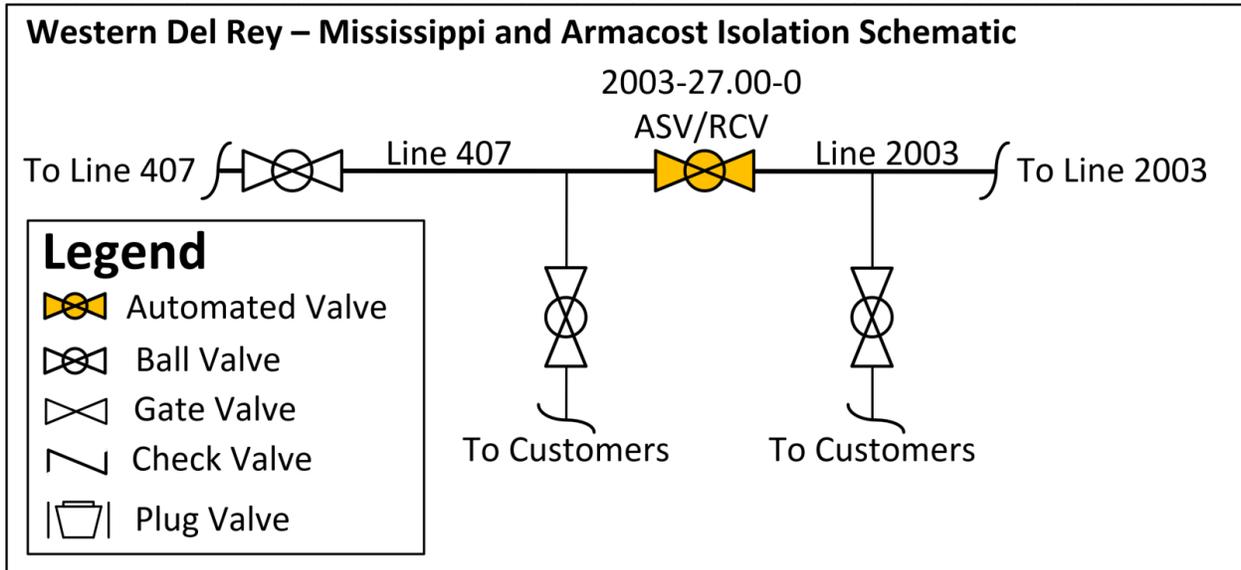

Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost

D. Scope Changes

SoCalGas did not make any notable scope changes during detailed design.

Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost

III. CONSTRUCTION

A. Construction Contractor Selection

The Project Team prepared an initial cost estimate based on the preliminary design. Following completion of the engineering, design, and planning activities described above, the Project Team directed the Alliance Partner (Electrical Contractor) to prepare cost estimates based on a more detailed engineering design package. As indicated above, there were no notable changes in scope between the time when the Project Team prepared the preliminary cost estimate and when the Performance Partner and Alliance Partner prepared and submitted their estimates.

1. SoCalGas' Preliminary Electrical Contractor Estimate (confidential): SoCalGas' preliminary cost estimate for construction was [REDACTED].
2. Electrical Contractor's Estimate (confidential): The Electrical Contractor's estimate was [REDACTED], which was [REDACTED] than SoCalGas' preliminary cost estimate.

B. Construction Schedule

Table 3: Construction Timeline

| | |
|------------------------------|------------|
| Construction Start Date | 12/06/2017 |
| Construction Completion Date | 4/15/2019 |
| Days on Site | 24 days |
| Commissioning Date | 09/24/2018 |

The Project Team completed all construction activities as soon as practicable prior to commissioning. SoCalGas' finalization of commissioning activities is dependent on electrical utility connections, and system and/or resource availability.

Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost

C. Changes During Construction

SoCalGas successfully mitigated conditions during construction in a manner that minimized potential impacts on project scope, cost, and schedule. As a result, these conditions did not result in any notable change orders.

Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost

Figure 4: Trenching to Access Existing Electrical Power



Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost

D. Commissioning and Site Restoration

Commissioning activities included site restoration, final inspections, and placement of the valve back into service. During this stage, SoCalGas successfully performed site acceptance testing and conducted point-to-point verification with SoCalGas Gas Control personnel for the newly-automated valve, and transferred ownership of the new equipment to Field Operations. Closeout activities included development of final drawings, the reconciliation package, and updates to company recordkeeping systems to reflect the completed scope of work. The site was commissioned on September 24, 2018, as summarized in Table 3.

Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost

IV. PROJECT COSTS

A. Cost Avoidance Actions

SoCalGas exercised due diligence in the design, planning, and construction activities for this project to minimize or avoid costs when prudent to do so. As discussed above, the Project Team reviewed existing records, communicated with external stakeholders, and conducted a site walk to incorporate the known site conditions in the project plan and design. Specific examples of cost avoidance actions taken on this project were:

1. Land Use: The Project Team utilized existing SoCalGas facilities and easements for construction avoiding the need to acquire additional land or easements.
2. Bundling of Projects: The Project Team bundled this project with the Western Del Rey Valve Enhancement Projects – McLaughlin and Palms and; Del Rey Junction, coordinating engineering, activities between the project sites.

B. Cost Estimates

Based on the preliminary design, once the preliminary project scope was confirmed and engineering, design, and planning activities were underway, SoCalGas prepared an estimate of the Direct Costs of the Project in the amount of \$708,641. The Project Team considered the conditions known at the time to prepare the preliminary Direct Cost estimate. This estimate reflects the projected Labor, Material, and Services costs anticipated to be incurred to execute the Project, based on initial design plans.

SoCalGas estimated Indirect Costs of the Project based on the estimated Direct Costs and other project-related variables.

C. Actual Direct and Indirect Costs

Actual Direct Costs reflect the Labor, Material, and Services costs incurred to execute the Project. Actual Indirect Costs reflect costs for incremental overhead loaders in

Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost

accordance with Company overhead allocation policies. The total loaded cost of the Project is \$494,984.

Table 4: Estimated and Actual Direct Costs and Variances²

| Direct Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|------------------------------------|----------------|----------------|--------------------|
| Company Labor | 187,365 | 42,512 | (144,853) |
| Materials | 49,674 | 62,343 | 12,669 |
| Mechanical Construction Contractor | 0 | 0 | 0 |
| Electrical Contractor | 171,248 | 104,647 | (66,601) |
| Construction Management & Support | 26,336 | 35,867 | 9,531 |
| Environmental | 22,624 | 0 | (22,624) |
| Engineering & Design | 117,368 | 114,607 | (2,761) |
| Project Management & Services | 53,395 | 1,211 | (52,184) |
| ROW & Permits | 732 | 615 | 118 |
| GMA | 79,898 | 53,960 | (25,938) |
| Total Direct Costs | 708,641 | 415,761 | (292,880) |

Table 5: Estimated and Actual Indirect Costs, Total Costs, and Variances³

| Indirect Costs/Total Costs (\$) ² | Estimate | Actuals | Delta Over/(Under) |
|--|------------------|----------------|--------------------|
| Overheads | 229,856 | 68,876 | (160,980) |
| AFUDC | 118,366 | 9,101 | (109,265) |
| Property Taxes | 27,191 | 1,245 | (25,946) |
| Total Indirect Costs | 375,413 | 79,223 | (296,190) |
| Total Direct Costs | 708,641 | 415,761 | (292,880) |
| Total Loaded Costs | 1,084,054 | 494,984 | (589,070) |

² Values may not add to total due to rounding.

³ Ibid.

Final Report Western Del Rey Valve Enhancement Project – Mississippi and Armacost

V. CONCLUSION

SoCalGas enhanced the safety of their integrated natural gas system by prudently executing the Western Del Rey Mississippi and Armacost Valve Enhancement Project. Through this Valve Enhancement Project, SoCalGas successfully automated one MLV to achieve the objective of enabling rapid system isolation in the City of Los Angeles. The total loaded cost of the Project is \$494,984.

SoCalGas executed this project prudently through designing and executing the project to support achievement of Valve Enhancement Plan isolation objectives, rebundling of projects for ease of cost and closeout trackability, and installing equipment necessary to bring communication capabilities to the site to enable rapid system isolation to a portion of Lines 2003 and 407.

SoCalGas engaged in prudent cost avoidance efforts to complete this safety enhancement at a reasonable cost by utilizing the existing utility power by carefully planning and coordinating construction activities to maximize efficiencies and reduce customer and community impacts.

End of Western Del Rey Valve Enhancement Project –Mississippi and Armacost Final Report

Final Report for Wilmington Valve Enhancement Project – Eubank Station

I. WILMINGTON VALVE ENHANCEMENT PROJECT – EUBANK STATION

A. Background and Summary

This report describes the activities associated with the Wilmington Valve Enhancement Project – Eubank Station site that consists of valve enhancements made to two existing valves located in the City of Wilmington. Through this project, SoCalGas enhanced the safety of its integrated gas transmission system by enabling the rapid detection of a significant change in pipeline pressure and remote isolation and depressurization of a portion of Line 1024 and Supply Line 43-1200 in the event of a pipeline rupture. SoCalGas installed new power equipment, new communications equipment, and the necessary automation equipment at the site. The total loaded project cost is \$796,028.

The Wilmington Valve Enhancement Project – Eubank Station construction site is within an existing SoCalGas facility in an area that is a mixture of industrial and residential development. SoCalGas bundled this valve project with an additional valve project, Wilmington Valve Enhancement Project – Lecouver and F Street, to gain efficiencies in engineering, planning and construction activities. This workpaper speaks to the Eubank Station site. This project was designed and executed as one cohesive project; however, the project costs were shared by PSEP and the Operating District with PSEP funding the activities that provided system isolation through automation of two valves and the Operating District funding the activities to install a new light pole and two new pressure transmitters.

Final Report for Wilmington Valve Enhancement Project – Eubank Station

Table 1: General Project Information

| Wilmington Valve Enhancement Project – Eubank Station | | | |
|--|--------------------|----------------|--------------|
| Location | City of Wilmington | | |
| Days on Site | 43 days | | |
| Construction Start | 03/19/2018 | | |
| Construction Finish | 06/14/2018 | | |
| Commissioning Date | 04/10/2019 | | |
| Valve Upgrades | | | |
| Valve Number | 1024-0.31-8 | | |
| Valve Type | Existing – Ball | | |
| Actuator | Existing | | |
| Actuator Above-/Below-Grade | Above-Grade | | |
| ASV | No | | |
| RCV | Yes | | |
| Valve Number | 1024-0.31-12 | | |
| Valve Type | Existing – Ball | | |
| Actuator | Existing | | |
| Actuator Above-/Below-Grade | Above-Grade | | |
| ASV | No | | |
| RCV | Yes | | |
| Site Upgrades | | | |
| Vault | None | | |
| Power | New – Utility | | |
| Communication | New – Radio | | |
| SCADA Panel | New | | |
| Equipment Shelter | None | | |
| Fencing/Wall | Yes – Existing | | |
| Project Costs (\$) | Capital | O&M | Total |
| Loaded Project Costs | 796,028 | - | 796,028 |
| Disallowed Costs | - | - | - |

Final Report for Wilmington Valve Enhancement Project – Eubank Station

B. Maps and Images

Figure 1: Wilmington Bundle Overview



Final Report for Wilmington Valve Enhancement Project – Eubank Station

Figure 2: Satellite Image of Wilmington Valve Enhancement Project – Eubank Station



Final Report for Wilmington Valve Enhancement Project – Eubank Station

II. ENGINEERING, DESIGN, AND PLANNING

A. Project Scope

SoCalGas presented a conceptual project scope in workpapers supporting the Valve Enhancement Plan in the 2011 PSEP filing.¹ This conceptual scope identified valves 1024-0.31-0 and 1024-1.62-2 for automation to enable remote isolation to portions of Line 1024. SoCalGas reviewed available information, performed a detailed system flow analysis, and determined that valves 1024-0.31-8 and 1024-0.31-12 were better candidates for enhancement to provide the planned isolation. The final project scope is summarized in Table 2 below.

1. 2011 PSEP Filing: SoCalGas identified valves 1024-0.31-0 and 1024-1.62-2 for automation to achieve the objective of rapid system isolation.
2. Updated Scope: Upon project initiation, SoCalGas reviewed the conceptual project scope and determined that these isolation points would not achieve the transmission isolation objectives set forth in the Valve Enhancement Plan. SoCalGas reevaluated the isolation points and determined that the automation of valves 1024-0.31-8 and 1024-0.31-12 would better achieve the objectives set forth in the Valve Enhancement Plan.
3. Engineering, Design, and Constructability: The Operating District requested that two pressure transmitters and a new light pole be installed at this facility. The Project Team incorporated this into the scope of work. The Operating District paid for the material and the installation of the pressure transmitters and the new light pole.
4. Final Project Scope: The final project scope consists of the automation of two valves, that included the installation of power equipment, the installation of communications equipment, and the installation of the necessary automation equipment at the site.

¹ See Workpapers supporting Amended Pipeline Safety Enhancement Plan (PSEP) of SoCalGas and SDG&E, submitted on December 2, 2011, at WP-IX-2-14 through WP-IX-2-25 (A.11-11-002 Exh. SCG-32).

Final Report for Wilmington Valve Enhancement Project – Eubank Station

Table 2: Final Project Scope

| Final Project Scope | | | | | |
|---------------------|------|---------|---------------------------------------|----------------------|----------|
| Line | Mile | Valve # | Valve Size (<i>confidential</i>) | Installation Type | Function |
| 1024 | 0.31 | 8 | | C/P | RCV |
| 1024 | 0.31 | 12 | | C/P | RCV |

B. Site Evaluation and Planning

SoCalGas initiated the planning process for the Wilmington Valve Enhancement Project – Eubank Station by performing a pre-design site walk to determine the existing conditions and assess any potential impact on the design. Key factors that influenced the engineering and design of this project are as follows:

1. Site Description: This site is an existing SoCalGas facility in an area that is a mixture of industrial and residential development.
2. Land Issues: During the pre-design site walk, the Project Team noted that the existing facility can accommodate the new equipment.
3. DOT Class: This project site is in a Class 3 location.
4. Power Source: There was no preexisting power equipment at the site. The Project Team installed new power equipment.
5. Communication Technology: There was no preexisting communications equipment. The Project Team installed new communications equipment at the site.

C. Engineering, Design, and Planning Factors


SoCalGas reviewed drawings and records, contacted internal planning groups, communicated with external stakeholders, conducted survey activity, and completed a site walk. Key factors that influenced the engineering and design of the Project are as follows:

Final Report for Wilmington Valve Enhancement Project – Eubank Station

1. Engineering Assessment: During the site evaluation, the Project Team confirmed the existing technology and verified that the station could accommodate the new equipment.
2. Valve Details:
 - a. 1024-0.31-8: The existing valve was a manually actuated Class 300 ball valve, which was reused by the Project Team.
 - b. 1024-0.31-12: The existing valve was a manually actuated Class 300 ball valve, which was reused by the Project Team.
3. Actuator Details:
 - a. 1024-0.31-8: The existing actuator was a pneumatic actuator, which was reused by the Project Team.
 - b. 1024-0.31-12: The existing actuator was a pneumatic actuator, which was reused by the Project Team.
4. Customer Impact: The Project Team did not anticipate service disruptions to customers.
5. Community Impact: The Project Team did not anticipate any notable impacts to the community from this project.
6. Substructures: The Project Team did not identify any existing substructures that affected the design and engineering at this site.
7. Environmental: The Project Team did not identify any notable environmental concerns at the site. An environmental monitor performed routine site visits during construction.
8. Permit Restrictions: There were no special permits or permit restrictions for this project site.
9. Land Use: The Project Team used the existing SoCalGas facility as a laydown yard.
10. Traffic Control: The Project Team did not identify any traffic needs control at this site.

Final Report for Wilmington Valve Enhancement Project – Eubank Station

Figure 3: Wilmington Valve Enhancement Project – Eubank Station Schematic

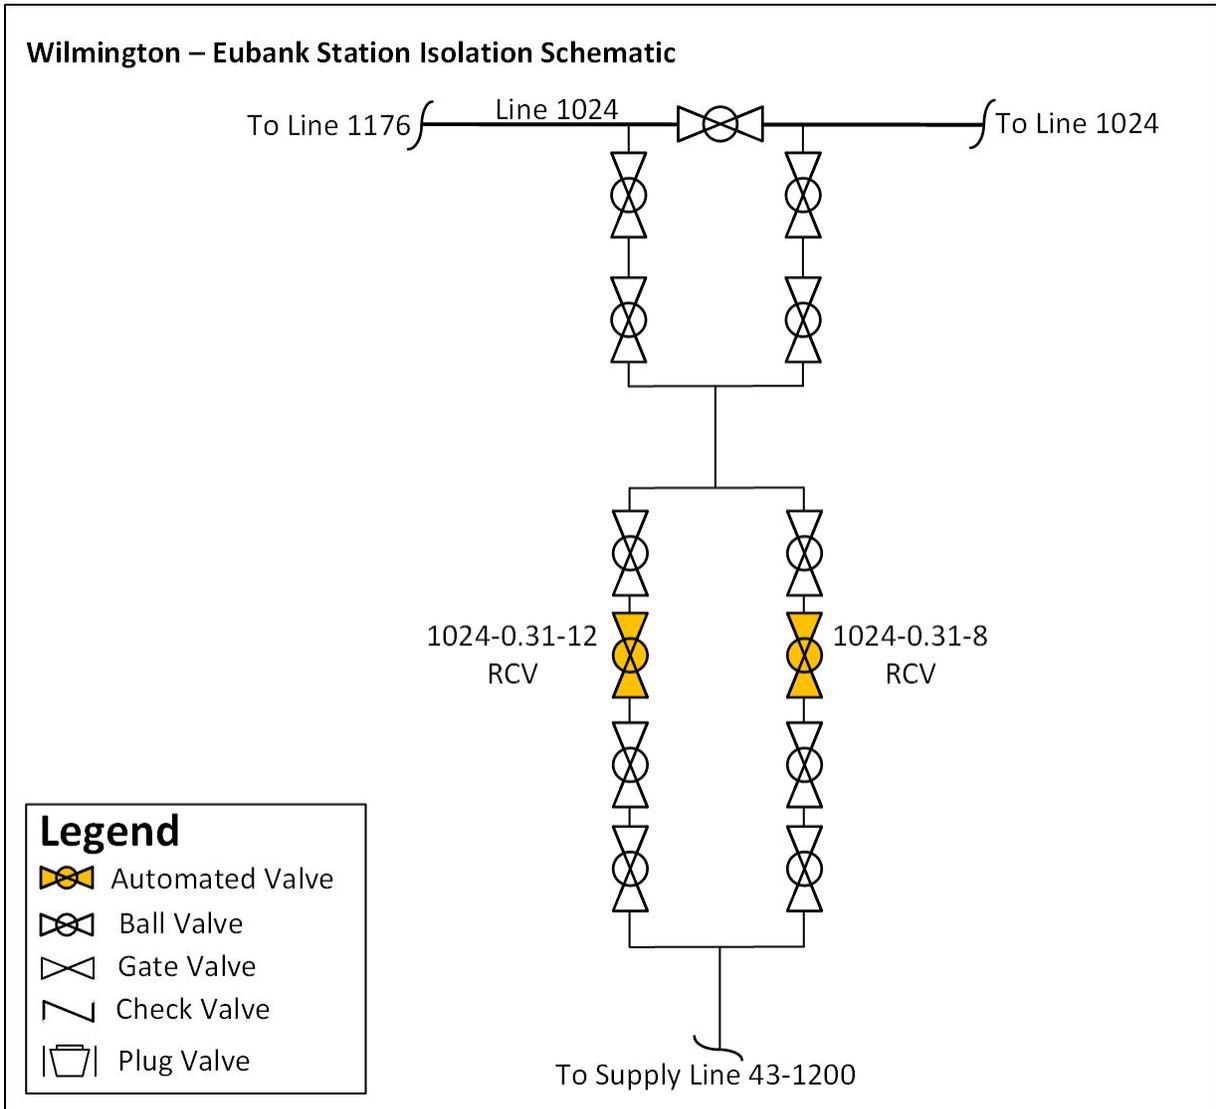

Final Report for Wilmington Valve Enhancement Project – Eubank Station

D. Scope Changes

SoCalGas did not make any notable scope changes during detailed design.

Final Report for Wilmington Valve Enhancement Project – Eubank Station

III. CONSTRUCTION

A. Construction Contractor Selection

The Project Team prepared an initial cost estimate based on the preliminary design. Following completion of the engineering, design, and planning activities described above, the Project Team directed the Alliance Partner (Electrical Contractor) to prepare cost estimates based on a more detailed engineering design package. As indicated above, there were no notable changes in scope between the time when the Project Team prepared the preliminary cost estimate and when the Alliance Partner prepared and submitted their estimate. The estimated values below represent the PSEP portion of the scope.

1. SoCalGas' Preliminary Electrical Contractor Estimate (confidential): SoCalGas' preliminary cost estimate for construction was [REDACTED].
2. Electrical Contractor's Estimate (confidential): The Electrical Contractor's estimate was [REDACTED], which was [REDACTED] than SoCalGas' preliminary cost estimate.

B. Construction Schedule

Table 3: Construction Timeline

| | |
|------------------------------|------------|
| Construction Start Date | 03/19/2018 |
| Construction Completion Date | 06/14/2018 |
| Days on Site | 43 days |
| Commissioning Date | 04/10/2019 |

The Project Team completed all construction activities as soon as practicable prior to commissioning. SoCalGas' finalization of commissioning activities is dependent on electrical utility connections, and system and/or resource availability.

Final Report for Wilmington Valve Enhancement Project – Eubank Station

C. Changes During Construction

SoCalGas successfully mitigated conditions during construction in a manner that minimized potential impacts on project scope, cost, and schedule. As a result, these conditions did not result in any notable change orders.

Final Report for Wilmington Valve Enhancement Project – Eubank Station

Figure 4: New Automation Equipment



Final Report for Wilmington Valve Enhancement Project – Eubank Station

D. Commissioning and Site Restoration

Commissioning activities included site restoration, final inspections, and placement of the valves back into service. During this stage, SoCalGas successfully performed site acceptance testing, and conducted point-to-point verification with SoCalGas Gas Control personnel for the newly-automated valves, and transferred ownership of the new equipment to Field Operations. Closeout activities included development of final drawings, the reconciliation package, and updates to company recordkeeping systems to reflect the completed scope of work. The site was commissioned on April 10, 2019, as summarized in Table 3.

Final Report for Wilmington Valve Enhancement Project – Eubank Station

IV. PROJECT COSTS

A. Cost Avoidance Actions

SoCalGas exercised due diligence in the design, planning, and construction activities for this project to minimize or avoid costs when prudent to do so. As discussed above, the Project Team reviewed existing records, communicated with external stakeholders, and conducted a site walk to incorporate the known site conditions in the project plan and design. SoCalGas grouped this site with one additional site, Wilmington Valve Enhancement Project – Lecouver and F Street, coordinating engineering and construction activities between the project sites to minimize costs for the benefit of customers.

B. Cost Estimates

Based on the preliminary design, once the preliminary project scope was confirmed and engineering, design, and planning activities were underway, SoCalGas prepared an estimate of the Direct Costs of the Project in the amount of \$1,002,562. The Project Team considered the conditions known at the time to prepare the preliminary Direct Cost estimate. This estimate reflects the projected Labor, Material, and Services costs anticipated to be incurred to execute the Project, based on initial design plans.

SoCalGas estimated Indirect Costs of the Project based on the estimated Direct Costs and other project-related variables.

C. Actual Direct and Indirect Costs

Actual Direct Costs reflect the Labor, Material, and Services costs incurred to execute the Project. Actual Indirect Costs reflect costs for incremental overhead loaders in accordance with Company overhead allocation policies. The total loaded cost of the Project is \$796,028.

Final Report for Wilmington Valve Enhancement Project – Eubank Station

Table 4: Estimated and Actual Direct Costs and Variances^{2, 3}

| Direct Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|------------------------------------|------------------|----------------|--------------------|
| Company Labor | 271,569 | 94,340 | (177,229) |
| Materials | 39,301 | 24,622 | (14,679) |
| Mechanical Construction Contractor | - | - | - |
| Electrical Contractor | 194,244 | 164,570 | (29,674) |
| Construction Management & Support | 39,192 | 91,137 | 51,945 |
| Environmental | 16,870 | 0 | (16,870) |
| Engineering & Design | 49,466 | 159,543 | 110,077 |
| Project Management & Services | 284,159 | 4,185 | (279,974) |
| ROW & Permits | 6,761 | 13,703 | 6,942 |
| GMA | 101,001 | 69,777 | (31,224) |
| Total Direct Costs | 1,002,562 | 621,878 | (380,684) |

Table 5: Estimated and Actual Indirect Costs, Total Costs, and Variances^{4, 5}

| Indirect Costs/Total Costs (\$) | Estimate | Actuals | Delta Over/(Under) |
|---------------------------------|------------------|----------------|--------------------|
| Overheads | 321,221 | 130,067 | (191,154) |
| AFUDC | 189,612 | 38,695 | (150,917) |
| Property Taxes | 43,543 | 5,388 | (38,155) |
| Total Indirect Costs | 554,376 | 174,150 | (380,226) |
| Total Direct Costs | 1,002,562 | 621,878 | (380,684) |
| Total Loaded Costs | 1,566,938 | 796,028 | (760,910) |

² Values may not add to total due to rounding.

³ Values in table represent PSEP costs only.

⁴ Values may not add to total due to rounding.

⁵ Values in table represent PSEP costs only.

Final Report for Wilmington Valve Enhancement Project – Eubank Station

V. CONCLUSION

SoCalGas enhanced the safety of their integrated natural gas system by prudently executing the Wilmington Valve Enhancement Project – Eubank Station. Through this Valve Enhancement Project, SoCalGas successfully automated two valves to achieve the objective of enabling rapid system isolation in the City of Wilmington. The total loaded cost of the Project is \$796,028.

SoCalGas executed this project prudently through designing and executing the project to support achievement of Valve Enhancement Plan isolation objectives, bundling two geographically proximate projects together to capture efficiencies through coordinated engineering, and by installing the equipment necessary to enable rapid system isolation to portions of Line 1024 and Supply Line 43-1200 in the City of Wilmington.

SoCalGas engaged in prudent cost avoidance efforts to complete this safety enhancement at a reasonable cost by carefully planning and coordinating engineering and construction activities to maximize efficiencies and reduce customer and community impacts, engaging in reasonable efforts to promote competitive and market based rates for contractor services and materials, and using a reasonable amount of company and contractor resources to complete this safety enhancement as soon as practicable.

End of Wilmington Valve Enhancement Project – Eubank Station Final Report
